


**CITY OF MADISON  
EARLY WARNING SIRENS  
- LONG RANGE PLAN -**

- 123 COMPLETED SIREN RANGE & NUMBER
- 123 EXISTING SIREN RANGE & NUMBER
- 123 PROPOSED SIREN RANGE & NUMBER

MAP UPDATED: 21 JUN 2013

M:\Maps\emerg\_plan\WarningSirens\LongRangeSirenPlan.dgn  
M:\Maps\emerg\_plan\WarningSirens\planning.pen

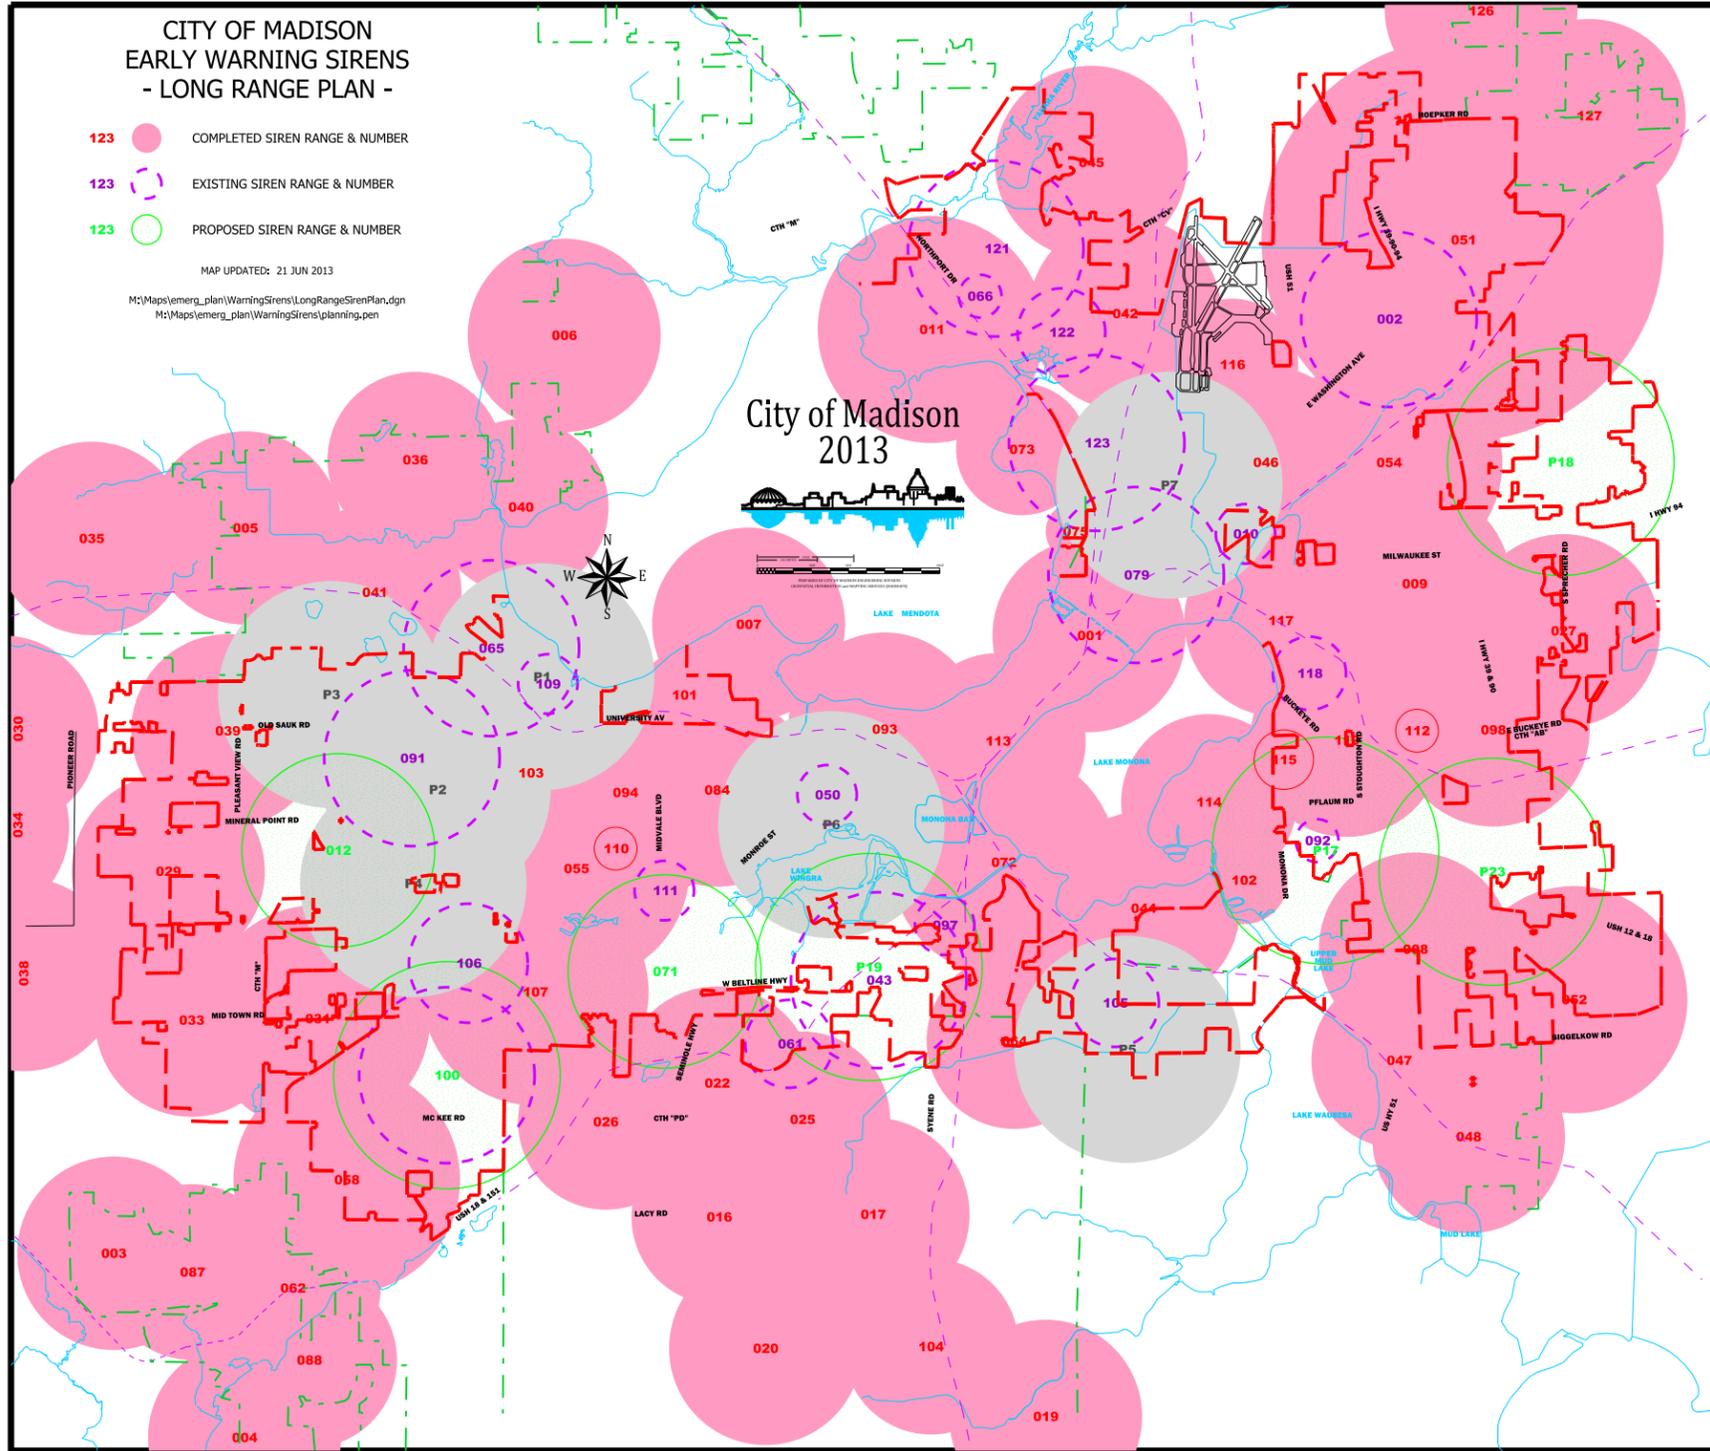

**INSTALLATION SCHEDULE**

MAPID	YEAR	RADIUS	PLAN SUMMARY & REMARKS	STATUS
052	2008	6200	NEW, STORCK RD	ACCEPTED JUNE 2009
072	2008	6200	NEW, SAYLE ST	ACCEPTED JUNE 2009
051	2008	11,000	NEW, EASTPARK BLVD (WISDOT PARK & RIDE LOT)	ACCEPTED OCTOBER 2009
011	2009	6200	NEW, TROY DR @ GREEN AVE	ACCEPTED NOVEMBER 2009
094	2009	6200	NEW, VAN HISE SCHOOL	ACCEPTED NOVEMBER 2009
029	2010	5280	NEW, SOUTH POINT RD, ENTRANCE TO WEST SIDE PUBLIC WORKS	ACCEPTED SEPTEMBER 2011
044	2010	5280	NEW, FRAZIER AVE	ACCEPTED SEPTEMBER 2011
007	2010	5280	NEW, LAKE MENDOTA DR	ACCEPTED SEPTEMBER 2011
042	2010	5280	NEW, PACKERS AVE	ACCEPTED SEPTEMBER 2011
084	2010	5280	NEW, EMERGENCY REPLACEMENT BY DCEM, LARKIN TOWER PARCEL	COMPLETED 2010 BY DCEM
045	2011	5280	NEW, N. SHERMAN AVE IN WEST R/W +/- 4400' NORTH OF WHEELER RD	ACCEPTED MAY 2012
008	2011	5280	NEW, VICINITY ENGINEERING PARCEL @ VOGES RD	ACCEPTED MAY 2012
001	2011	5280	NEW, VICINITY ENGINEERING PARCEL ON S. DICKINSON ST	ACCEPTED MAY 2012
009	2011	5280	NEW EMERGENCY REPLACEMENT BY DCEM, KENNEDY SCHOOL	COMPLETED 2011 BY DCEM
064	2011	4800	MOVED EXISTING FOR DEVELOPMENT FROM E. BADGER RD TO ENGELHART DR	COMPLETED 2011 BY DCEM
103	2012	6200	UPGRADED & RELOCATED DUE TO N ROSA RD PROJECT REGENT @ ROSA	COMPLETED 2012 BY DCEM
116	2012	3600	SIREN UPGRADED & RELOCATED TO OFF AIR BASE LOCATION	COMPLETED 2012 BY DCEM
P1	2013	6200	NEW, VICINITY UNIVERSITY AVE @ NORMAN WAY (REUSE 109)	
P2	2013	6200	NEW, VICINITY MINERAL POINT LANDFILL (REUSE 091)	
P3	2013	6200	NEW, N. HIGH POINT RD @ TRAMORE TRL	
P4	2013	6200	NEW, VICINITY S. GAMMON RD @ SEYBOLD RD (REUSE 106)	
P5	2013	6200	NEW, VICINITY LAKE FARM RD @ LIBBY RD (REUSE 105)	
P6	2013	6200	NEW, VICINITY OF VILAS PARK DR, ZOO & BEACH AREA (REUSE 050)	
P7	2013	6200	NEW, VICINITY OF ABERG & SHOPKO DR	
P17	2014	6200	NEW, VICINITY EDNA TAYLOR PARK (CORNER WOODLAWN DR)	EXPLORE COST SHARE WITH MONONA
071	NLT 2014	6200	SIREN UPGRADED BY DCEM IN 2011 RELOCATE DUE TO WISDOT PROJECT	RELOCATION BY DCEM
012	NLT 2015	5280	SIREN UPGRADED IN 2004 BY DCEM; RELOCATE DUE TO WISDOT PROJECT	RELOCATION BY DCEM
P19	TBD	6200	NEW, WEST END OF WEST BADGER RD (STREETS DEPT @ RR)	
100	TBD	6200	UPGRADE AND RELOCATE TO NEW SITE TBD	
P18	TBD	6200	NEW, VICINITY REINER RD, 1/2 MILE NORTH OF CTH T (COMMERCIAL)	PENDING DEVELOPMENT
P23	TBD	6200	NEW, VICINITY WATER UTILITY PARCEL, FEMRITE DRIVE	

**DECOMMISSIONING & REMOVAL SCHEDULE BY DCEM**

YEAR	MAPID	PLAN SUMMARY & REMARKS	STATUS
2009	o-114, o-122	OLD 114 TURNED OVER TO MENDOTA, OLD 122 REMOVED	COMPLETED
2010	o-186	OFF LINE FOR TESTING IN 2009, REMOVAL IN 2010	
2011	o-163, o-164	OFF LINE FOR TESTING 2009, REMOVED IN 2011	COMPLETED
2011	o-112, o-113	o-112/o-113 FAILED, BOTH REPLACED WITH NEW o-112, REMOVALS IN 2012	COMPLETED
2011	o-107, o-162, o-195	PARTS SALVAGED IN 2010 CONTRACT RE-USED NUMBERS, REMOVE REMAINDER	162, 195 COMPLETED
2012	o-115, o-135	o-135 REPLACED IN 2010, o-115 OFF LINE/TESTING IN 2011, REMOVALS IN 2012	
2012	o-181	PARTS SALVAGED IN 2011 CONTRACT RE-USED NUMBER, REMOVE REMAINDER	COMPLETED
2013	o-109, o-179, o-172	OFF LINE AND TESTING IN 2013, REMOVAL IN 2014	
2014	o-129, o-148, o-197	OFF LINE AND TESTING IN 2014, REMOVAL IN 2015	
2015	o-166, o-169, o-171	OFF LINE AND TESTING IN 2015, REMOVAL IN 2016	
2016	o-105, o-145, o-175	OFF LINE AND TESTING IN 2016, REMOVAL IN 2017	
	o-101, o-156, o-177	REMOVALS DEPENDENT ON SOUND TESTING OF COMPLETED INSTALLATIONS	

**MISCELLANEOUS SYSTEM UPGRADES NOT SCHEDULED**

64	NEW, LONG RANGE, UPGRADE EXISTING IN PLACE	121	NEW, LONG RANGE, UPGRADE EXISTING IN PLACE
123	NEW, MEDIUM RANGE, TO UPDATE EXISTING		
NEW	LONG RANGE NEAR AG DRIVE, DECOM 178?		

**NOTES**

- ALL LOCATIONS ARE APPROXIMATE. ANNUAL TESTING OF EXISTING CONDITIONS WILL DETERMINE THE FINAL LOCATION FOR FUTURE SIRENS.
- EXCEPT AS NOTED IN THE CHART ABOVE ALL DECOMMISSIONING AND REMOVAL OF SIRENS SHALL ONLY BE COMPLETED AFTER TESTING AND NEIGHBORHOOD FEEDBACK.
- DCEM HAS THE FINAL DECISION ON DECOMMISSIONING ANY SIREN.
- NEW CONTROLS CONTRACT BY DCEM IN 2012, CONTRACTOR RENUMBERED ALL COUNTY SIRENS. NEW NUMBERS ARE SHOWN ON MAP EXCEPT WHERE THE PREFIX OF AN "o-" IS USED.
