




JOINT CAMPUS AREA COMMITTEE REVIEW - RECOMMENDATION



19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020




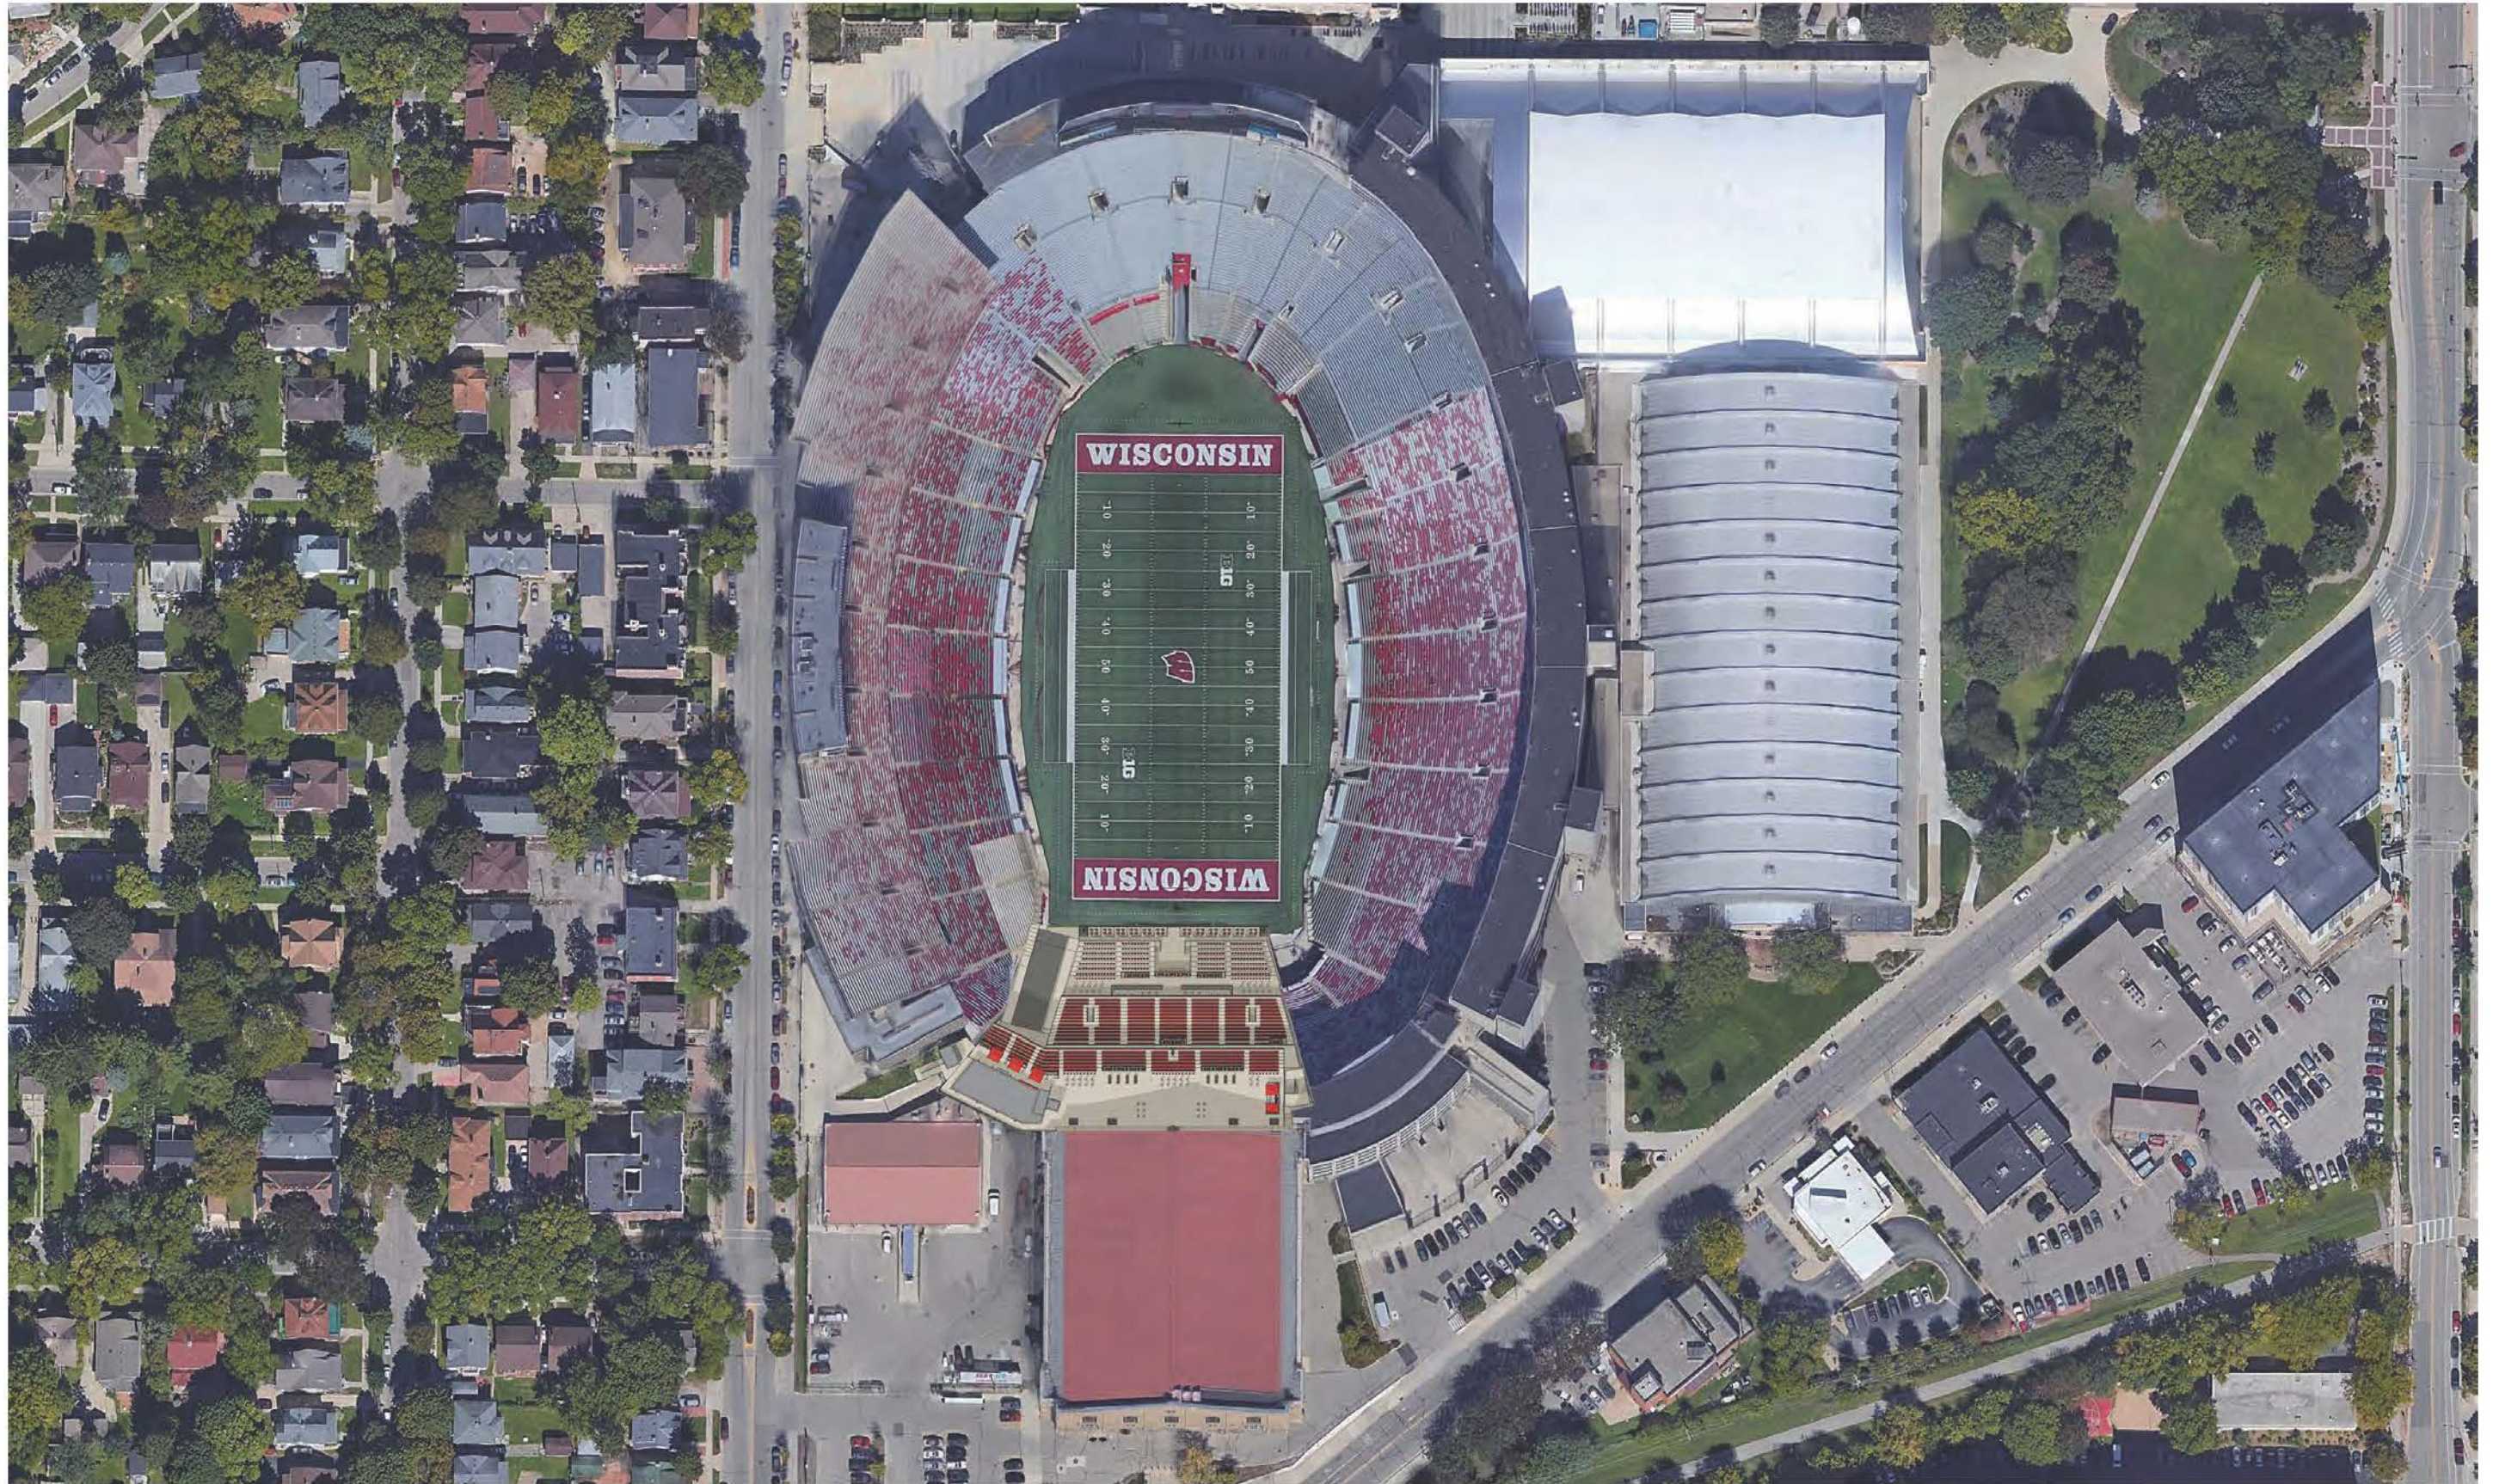

PROJECT | SITE PLAN VIEW

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020




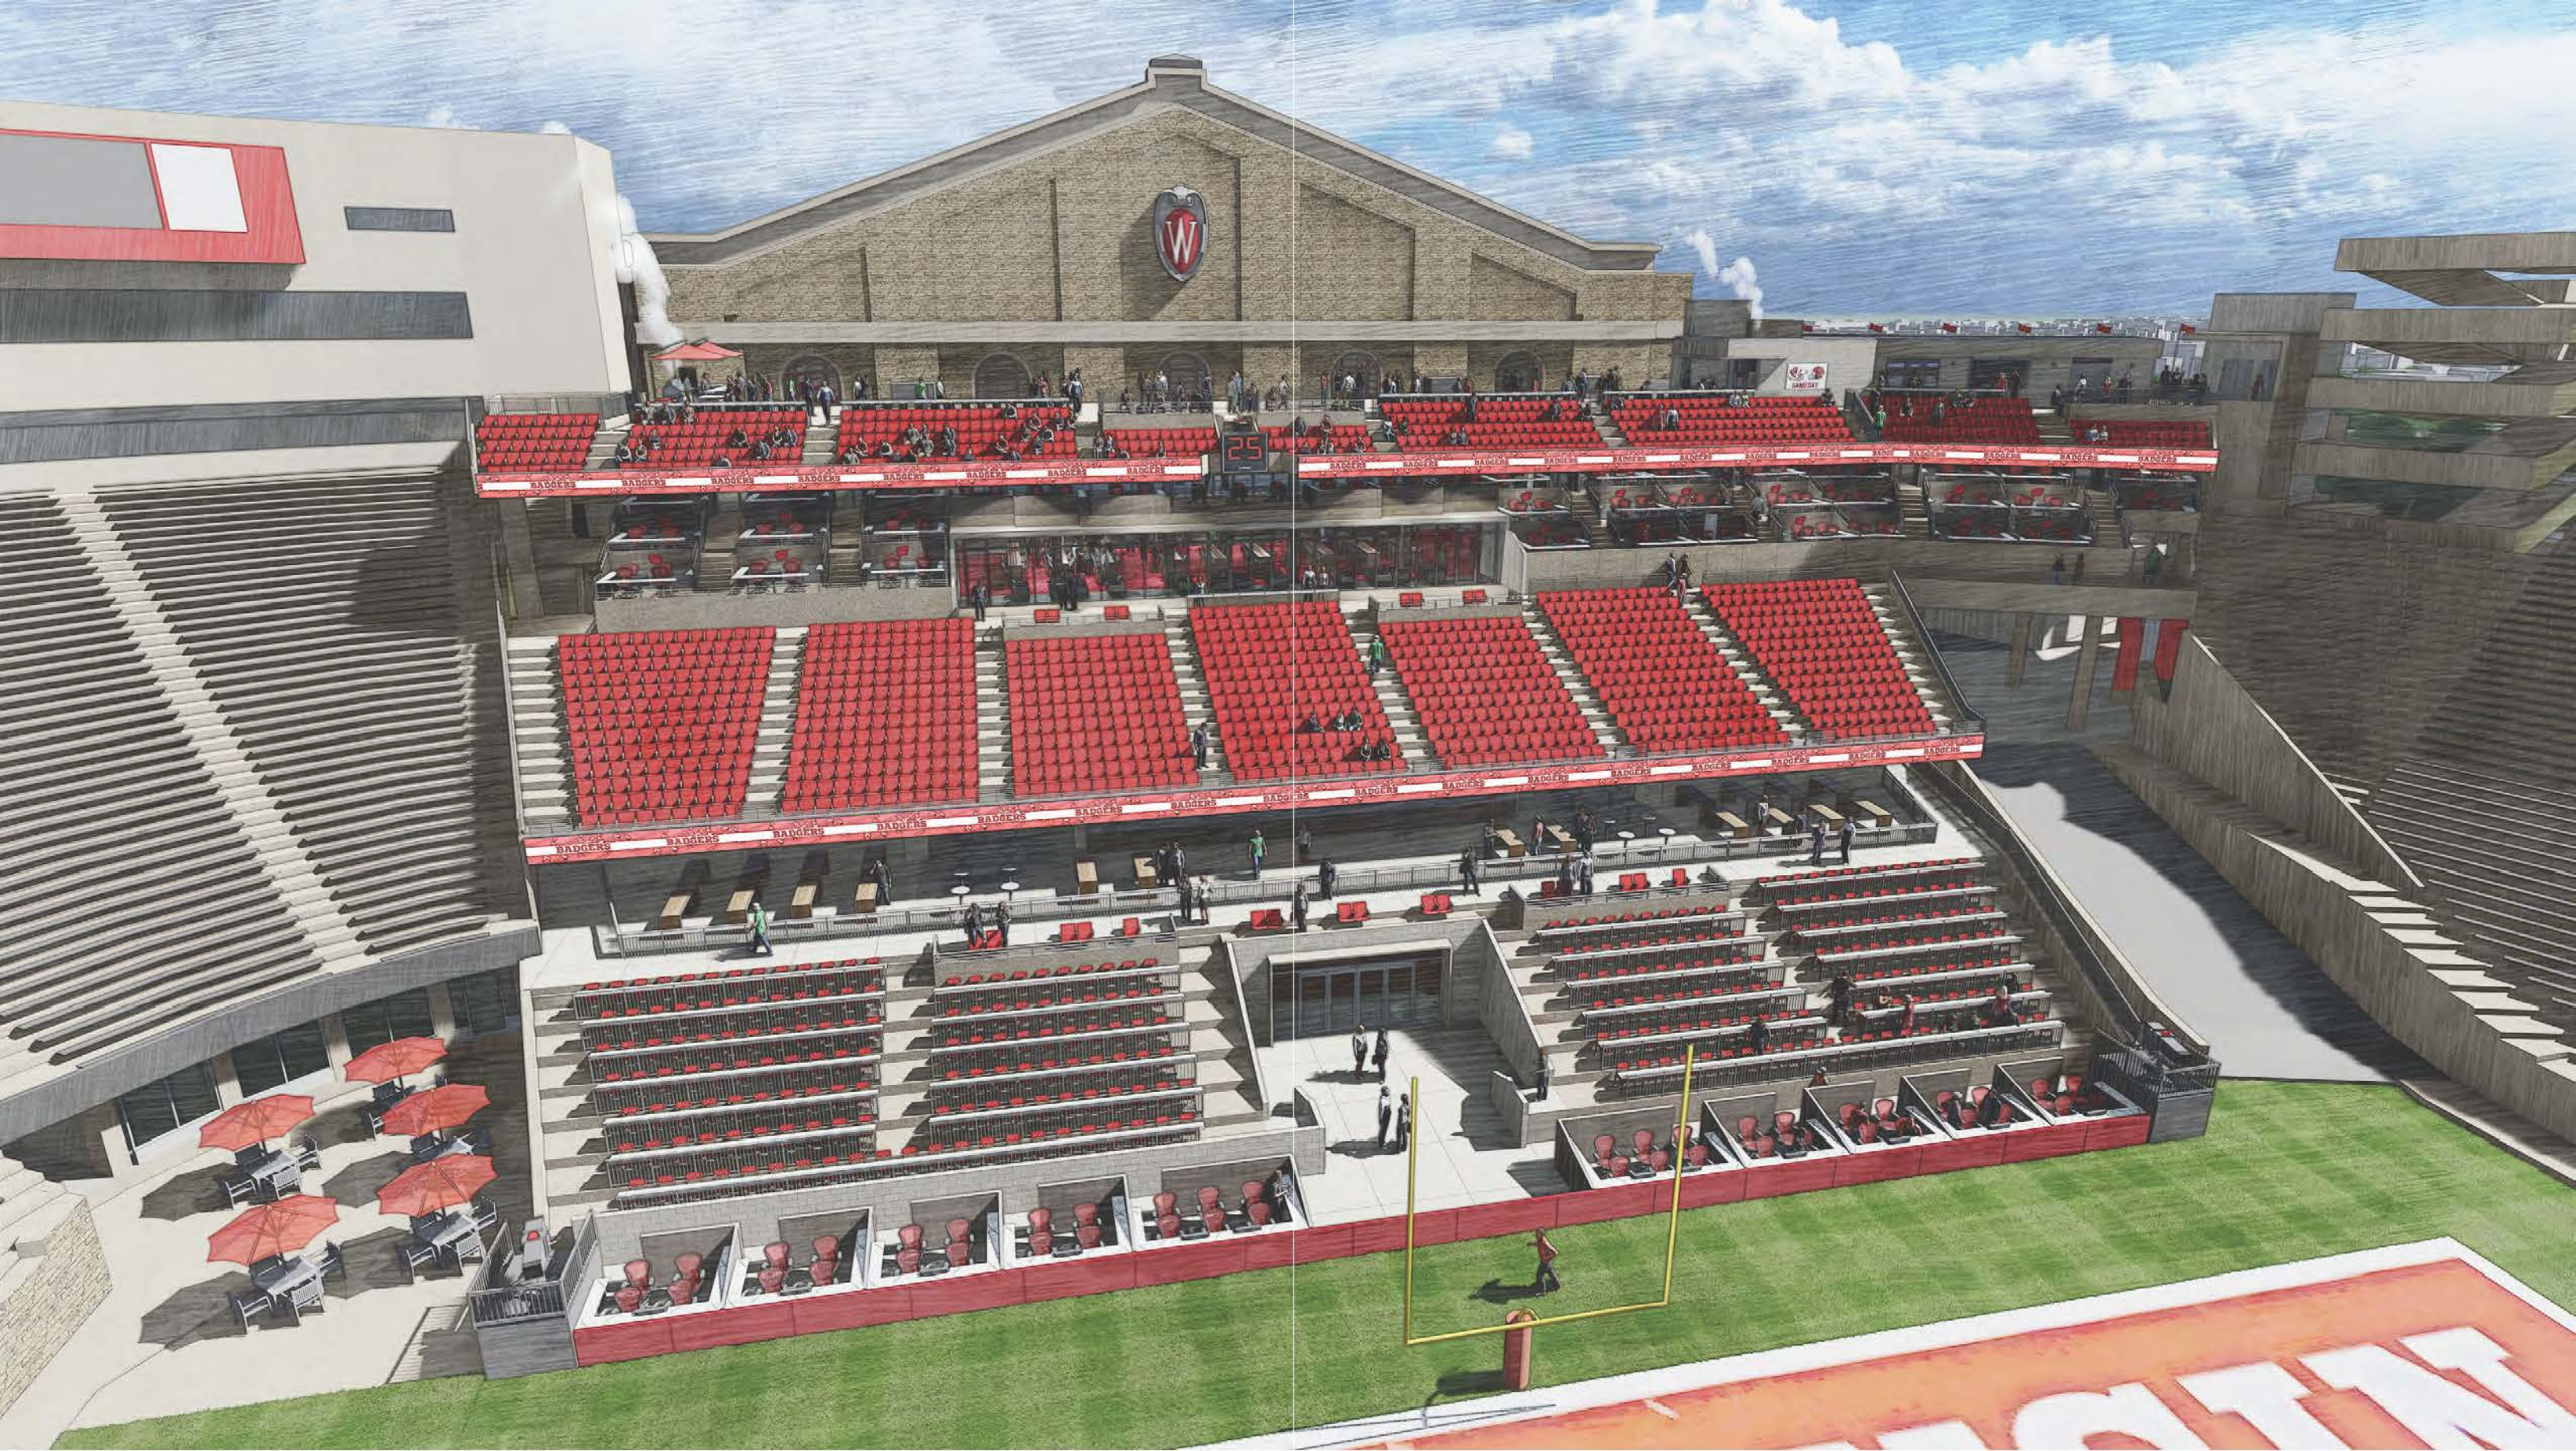

AERIAL | PERSPECTIVE VIEW

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020



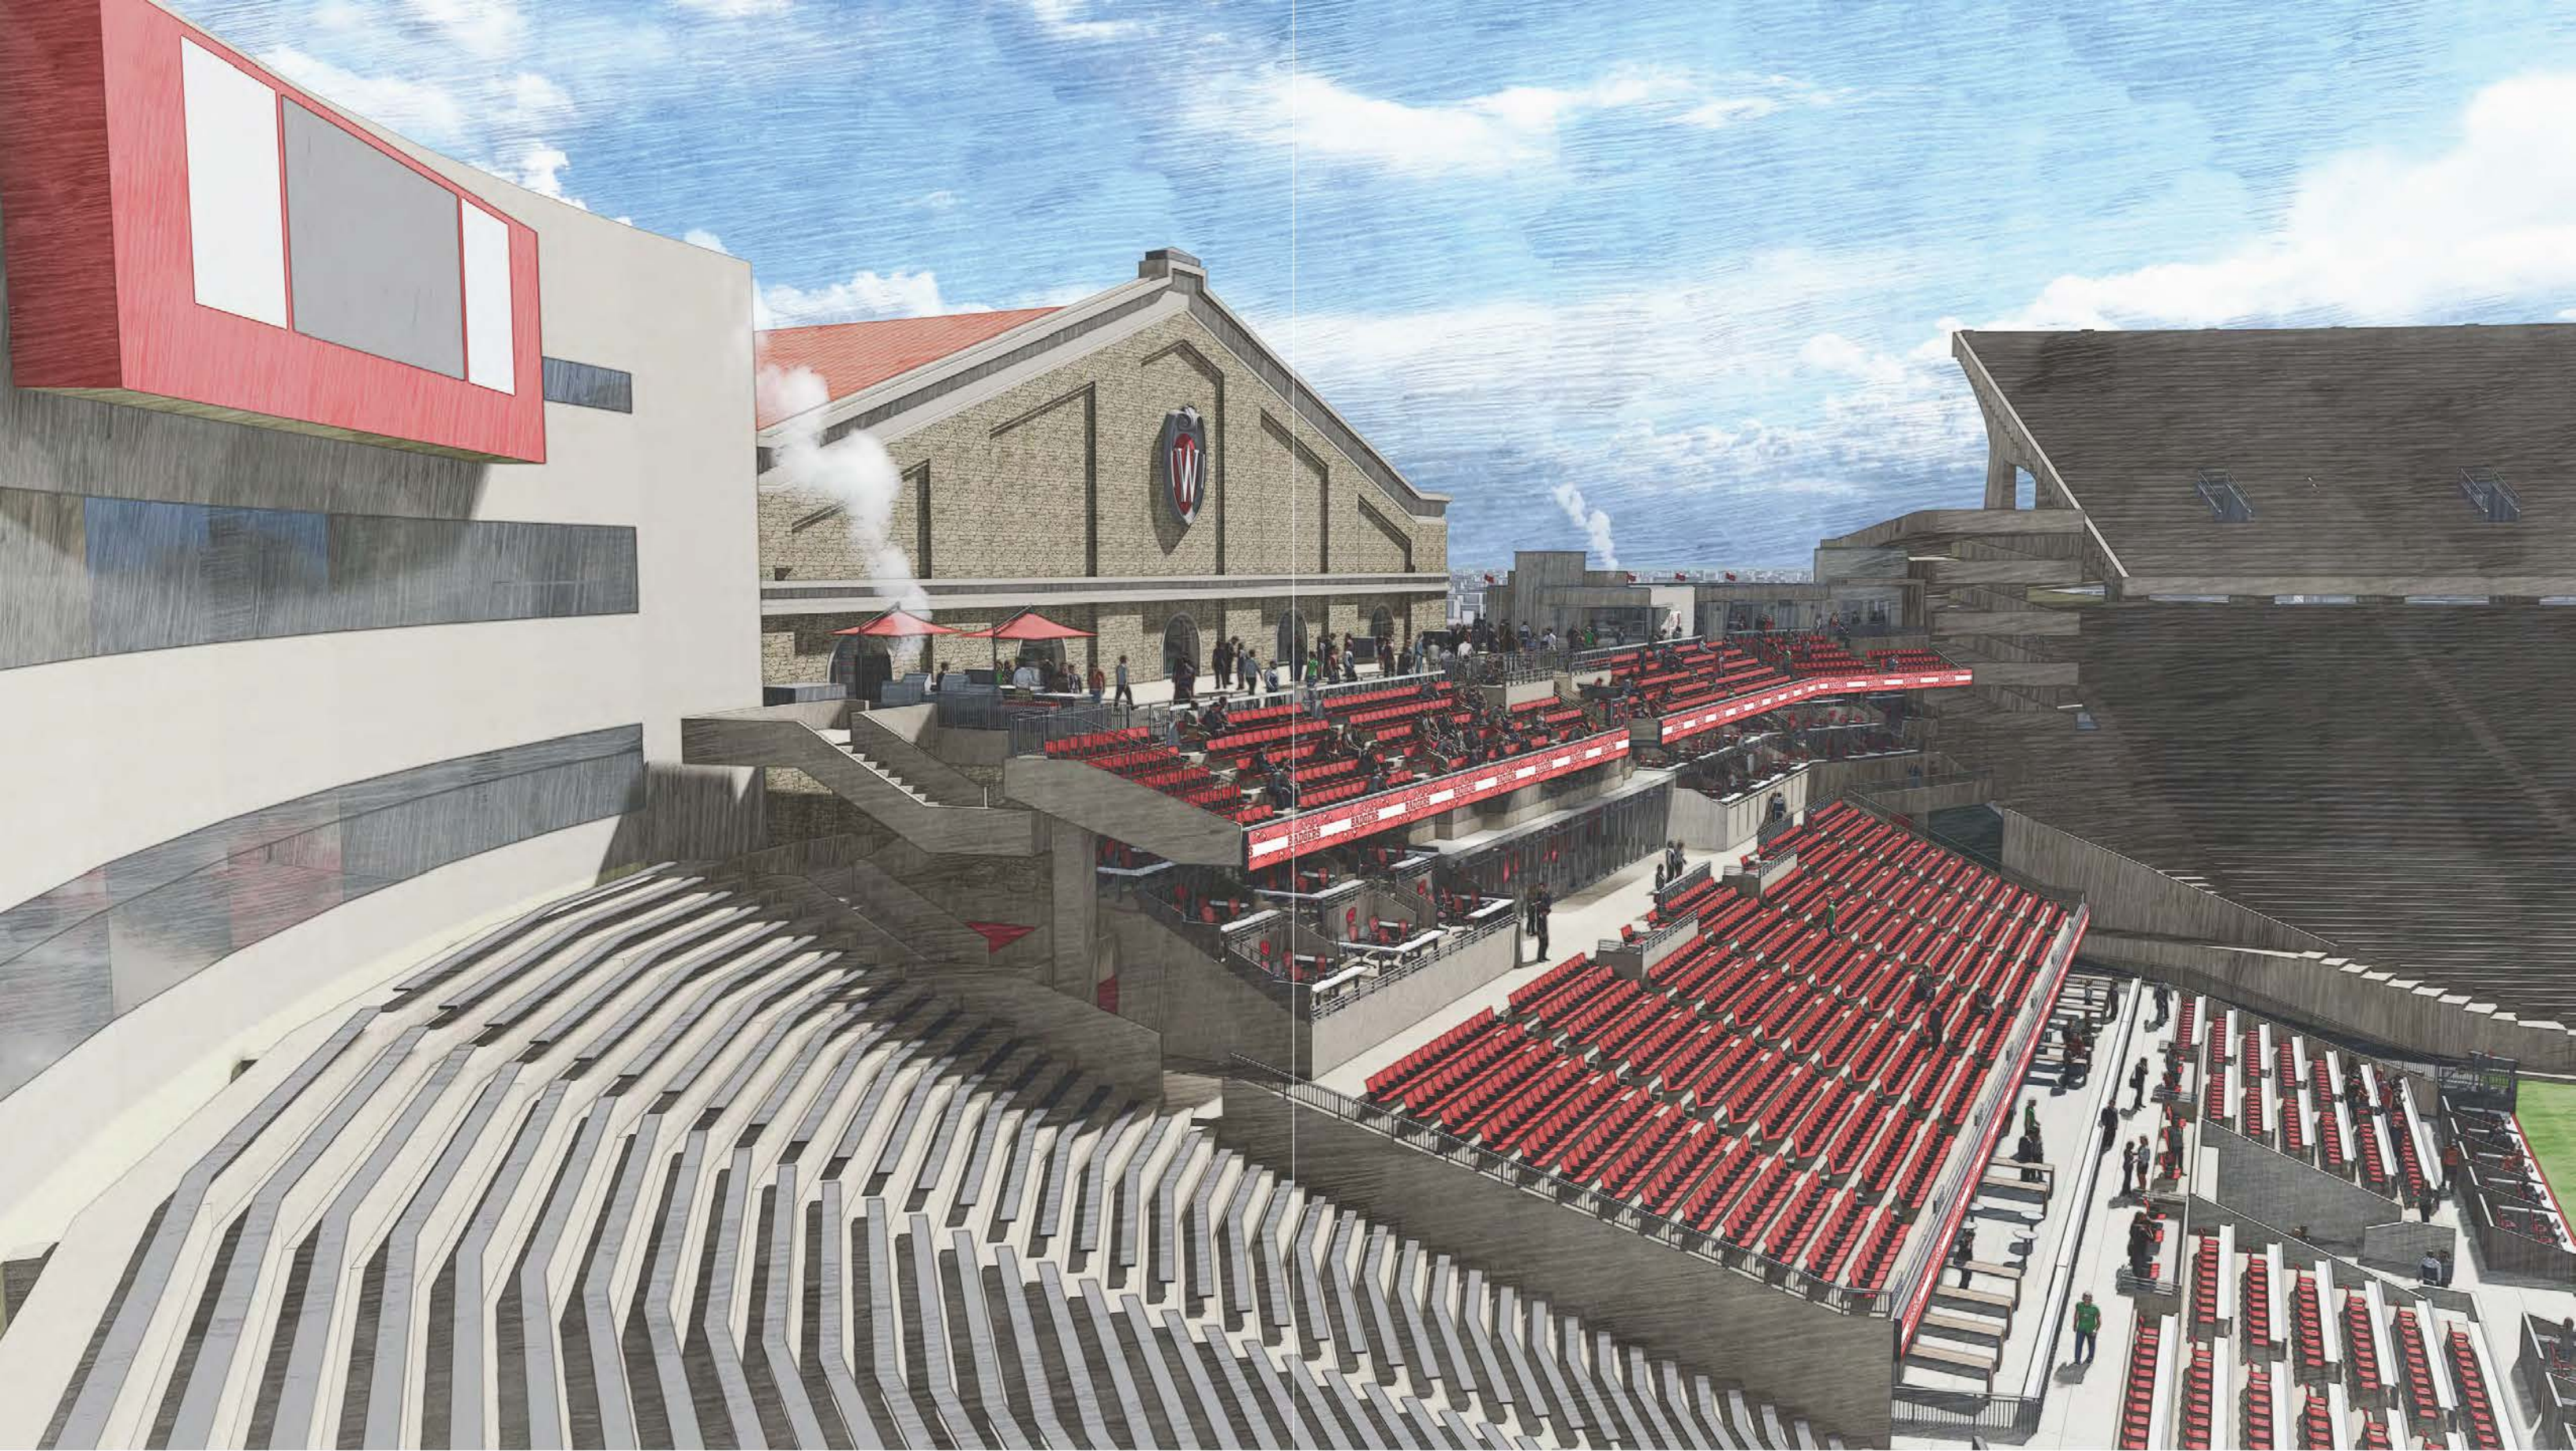


VIEW FROM EAST STANDS | PERSPECTIVE VIEW



19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020




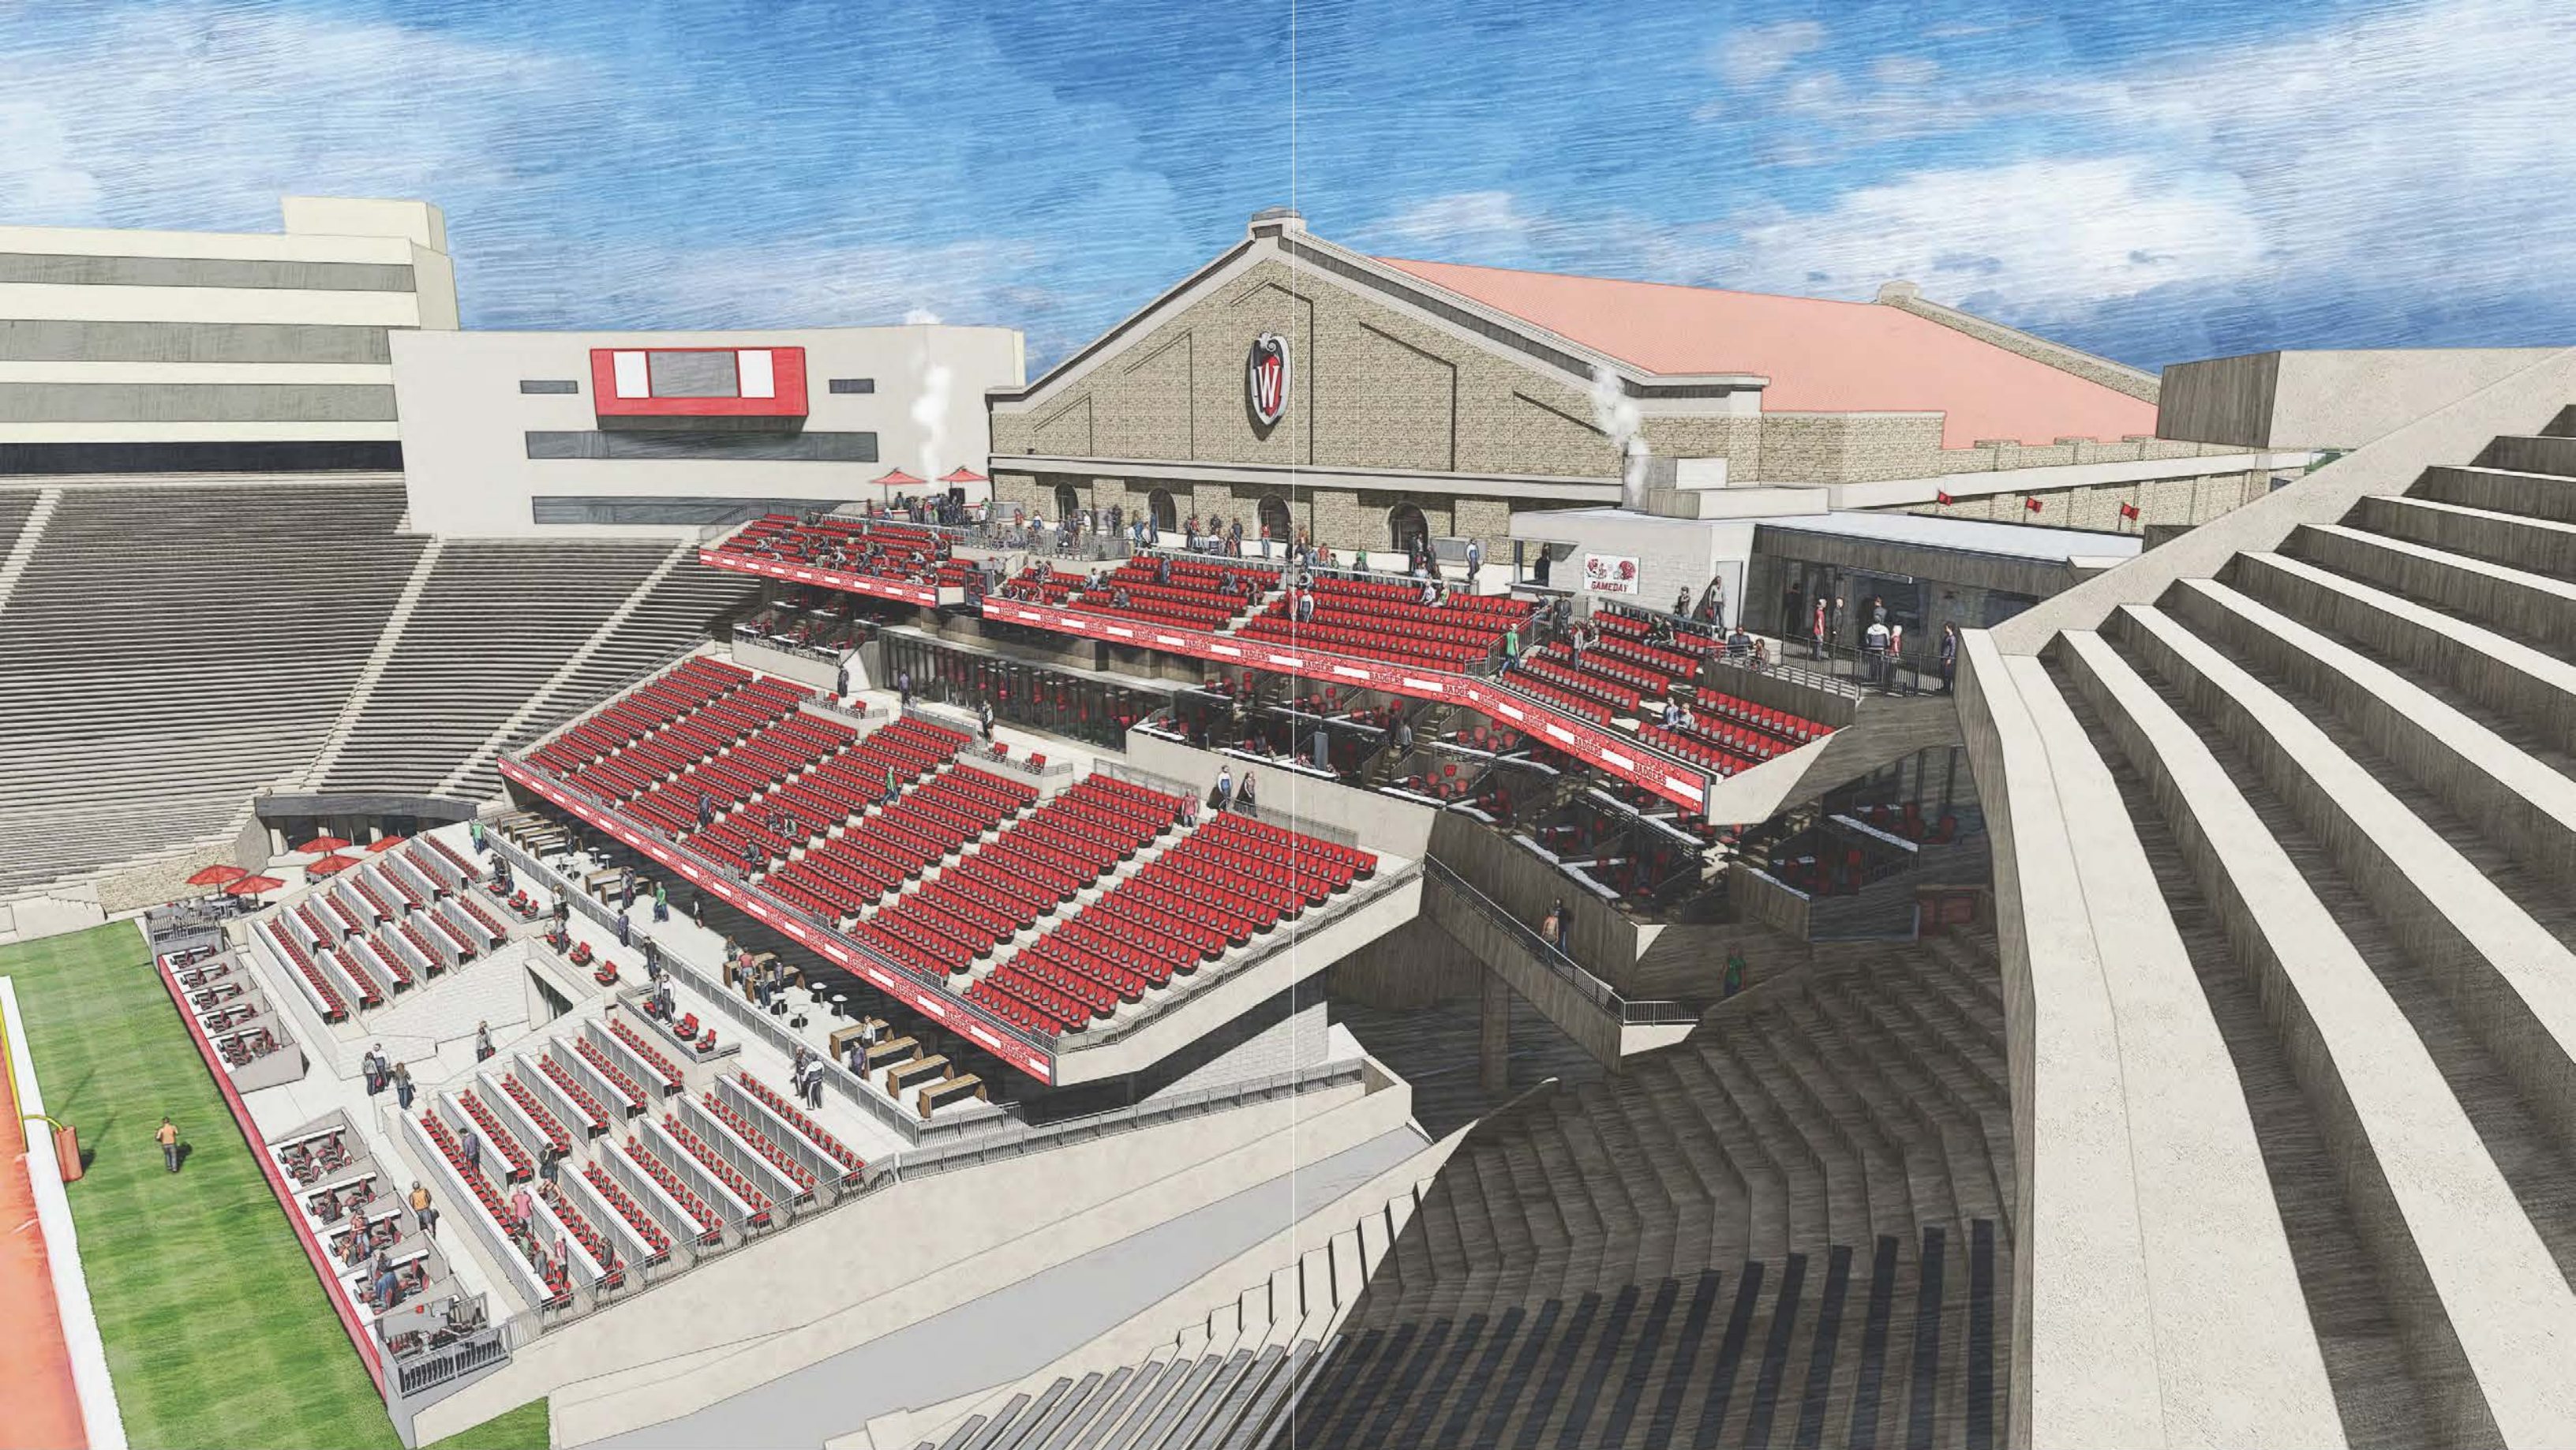

VIEW FROM WEST STANDS | PERSPECTIVE VIEW

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020



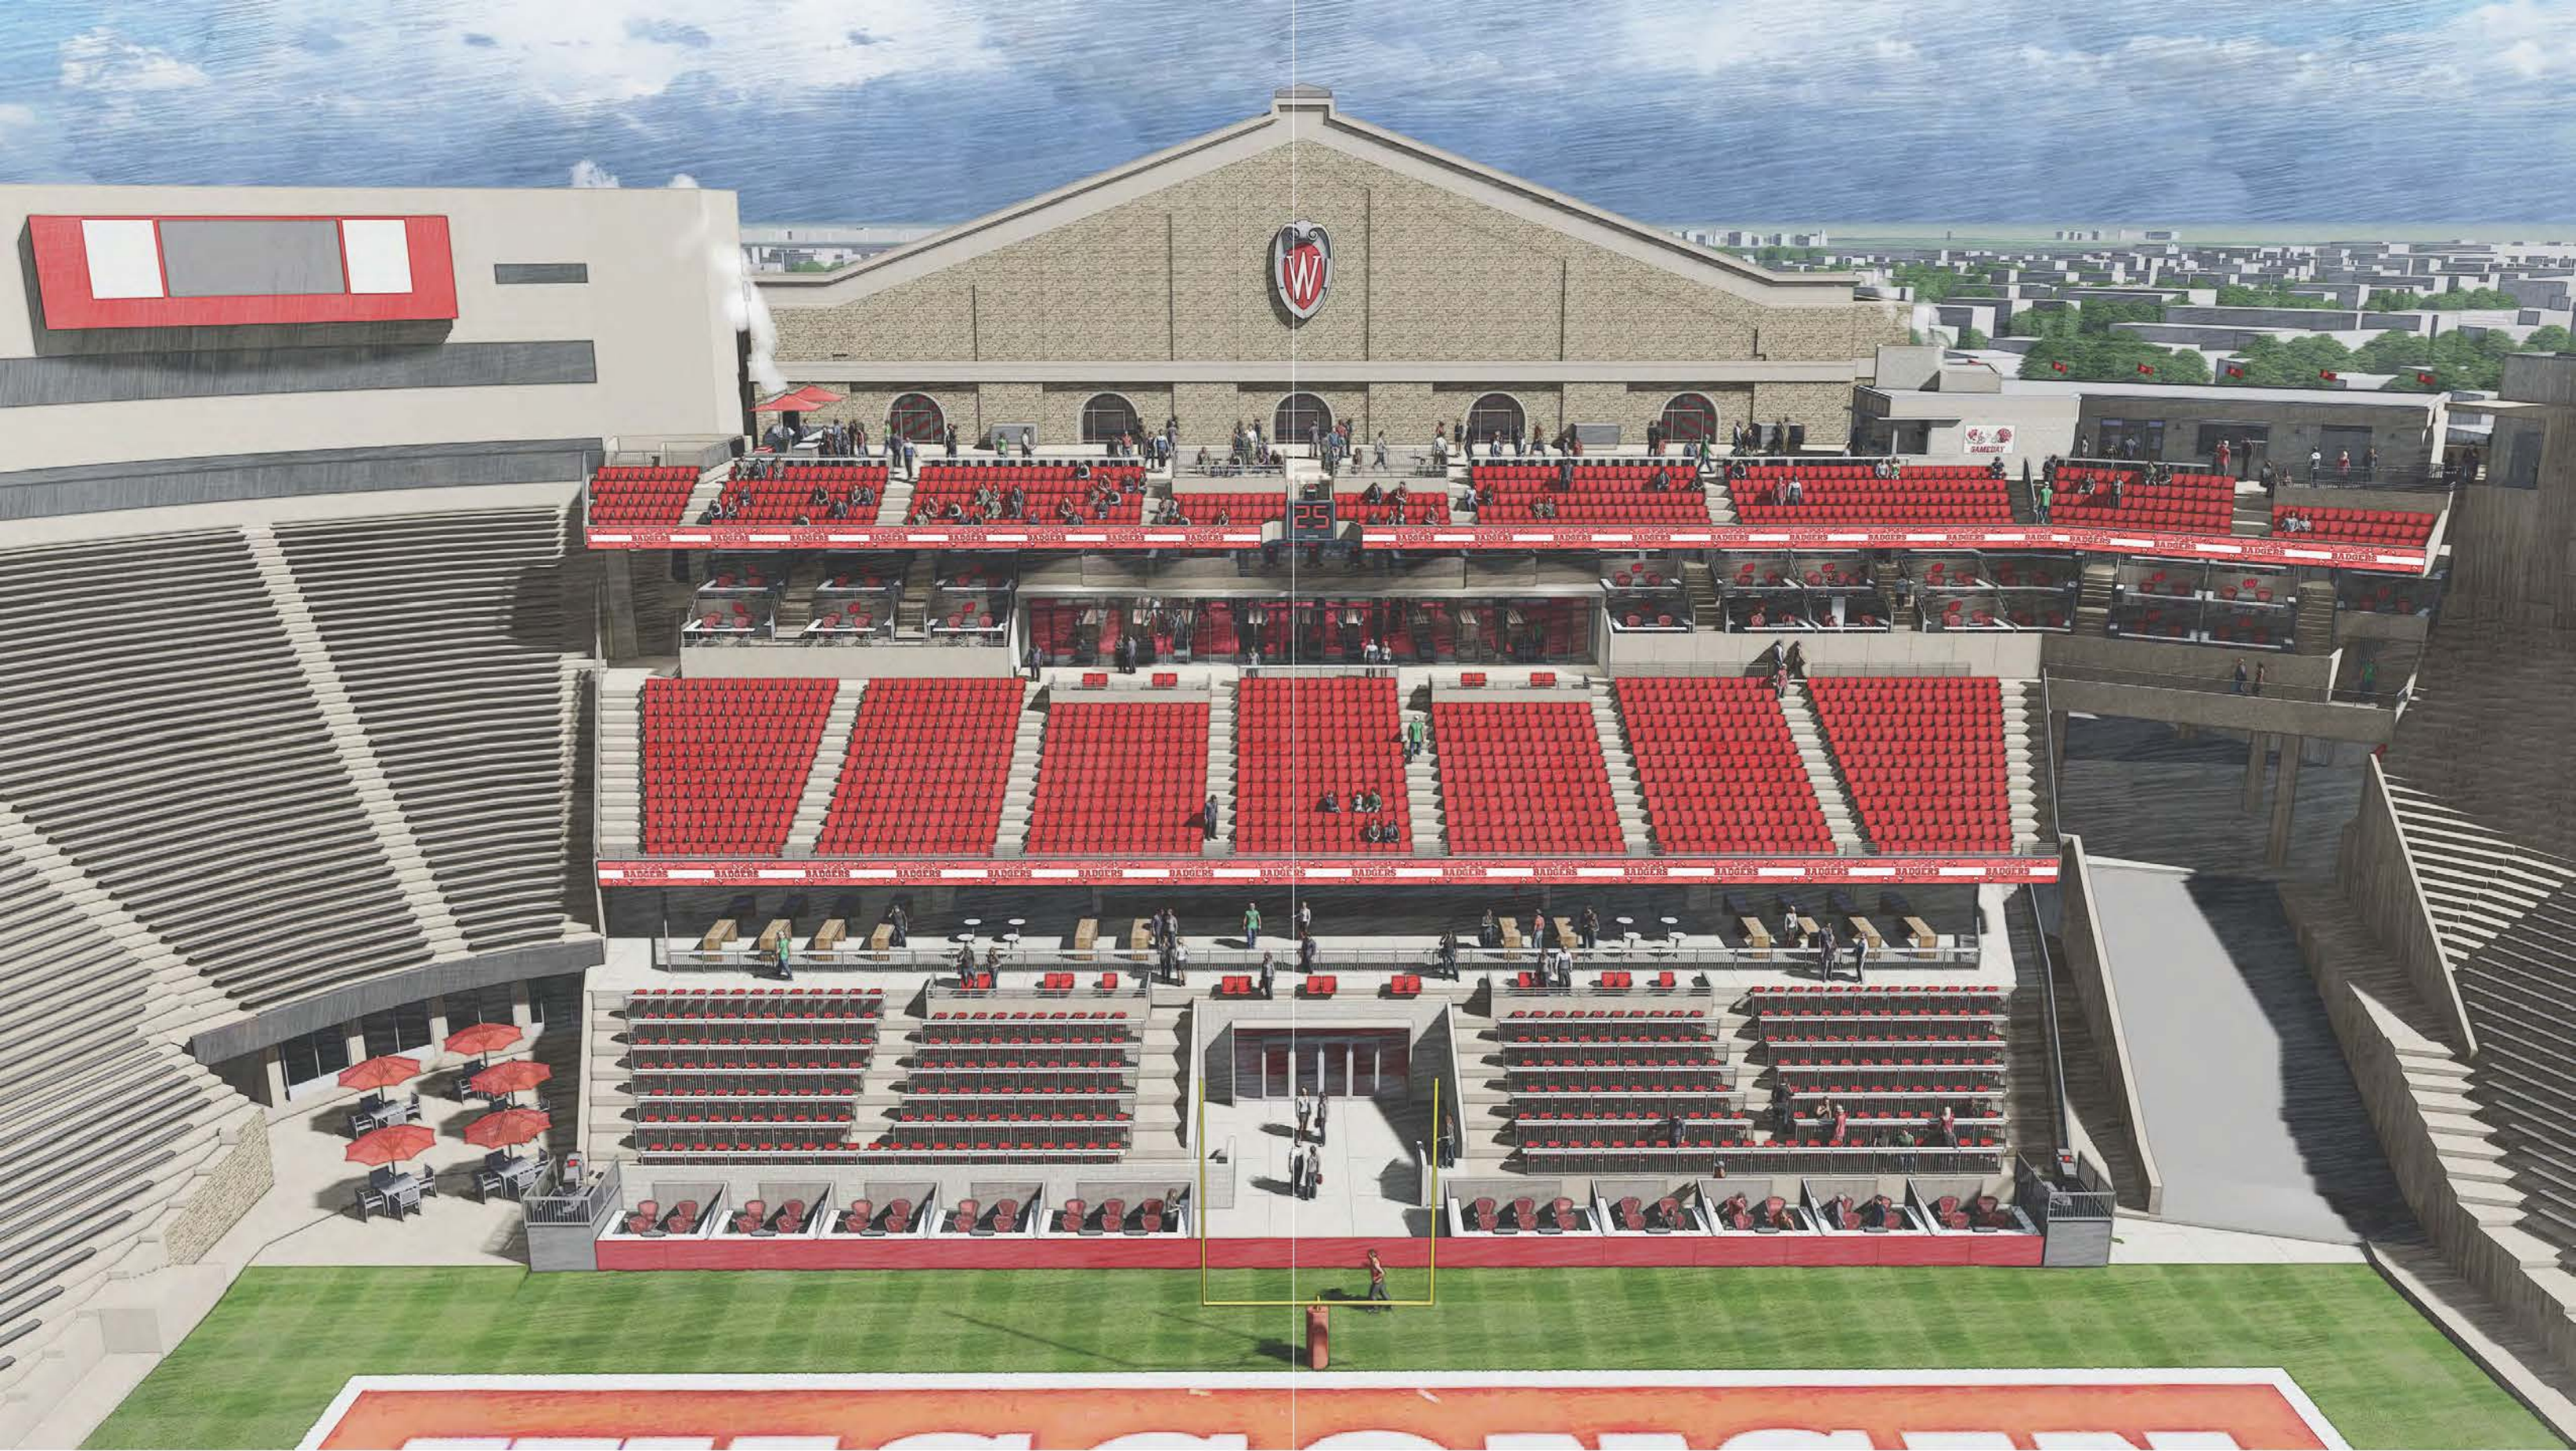

FRONT AERIAL | PERSPECTIVE VIEW

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020





VIEW OF UPPER TERRACE | PERSPECTIVE VIEW



19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020





SW EYE LEVEL VIEW 1 | EXISTING

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020





SW EYE LEVEL VIEW 1 | PROPOSED

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020





SW EYE LEVEL VIEW 2 | EXISTING

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020





SW EYE LEVEL VIEW 2 | PROPOSED

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020






FIELD LEVEL | FLOOR PLAN VIEW

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020




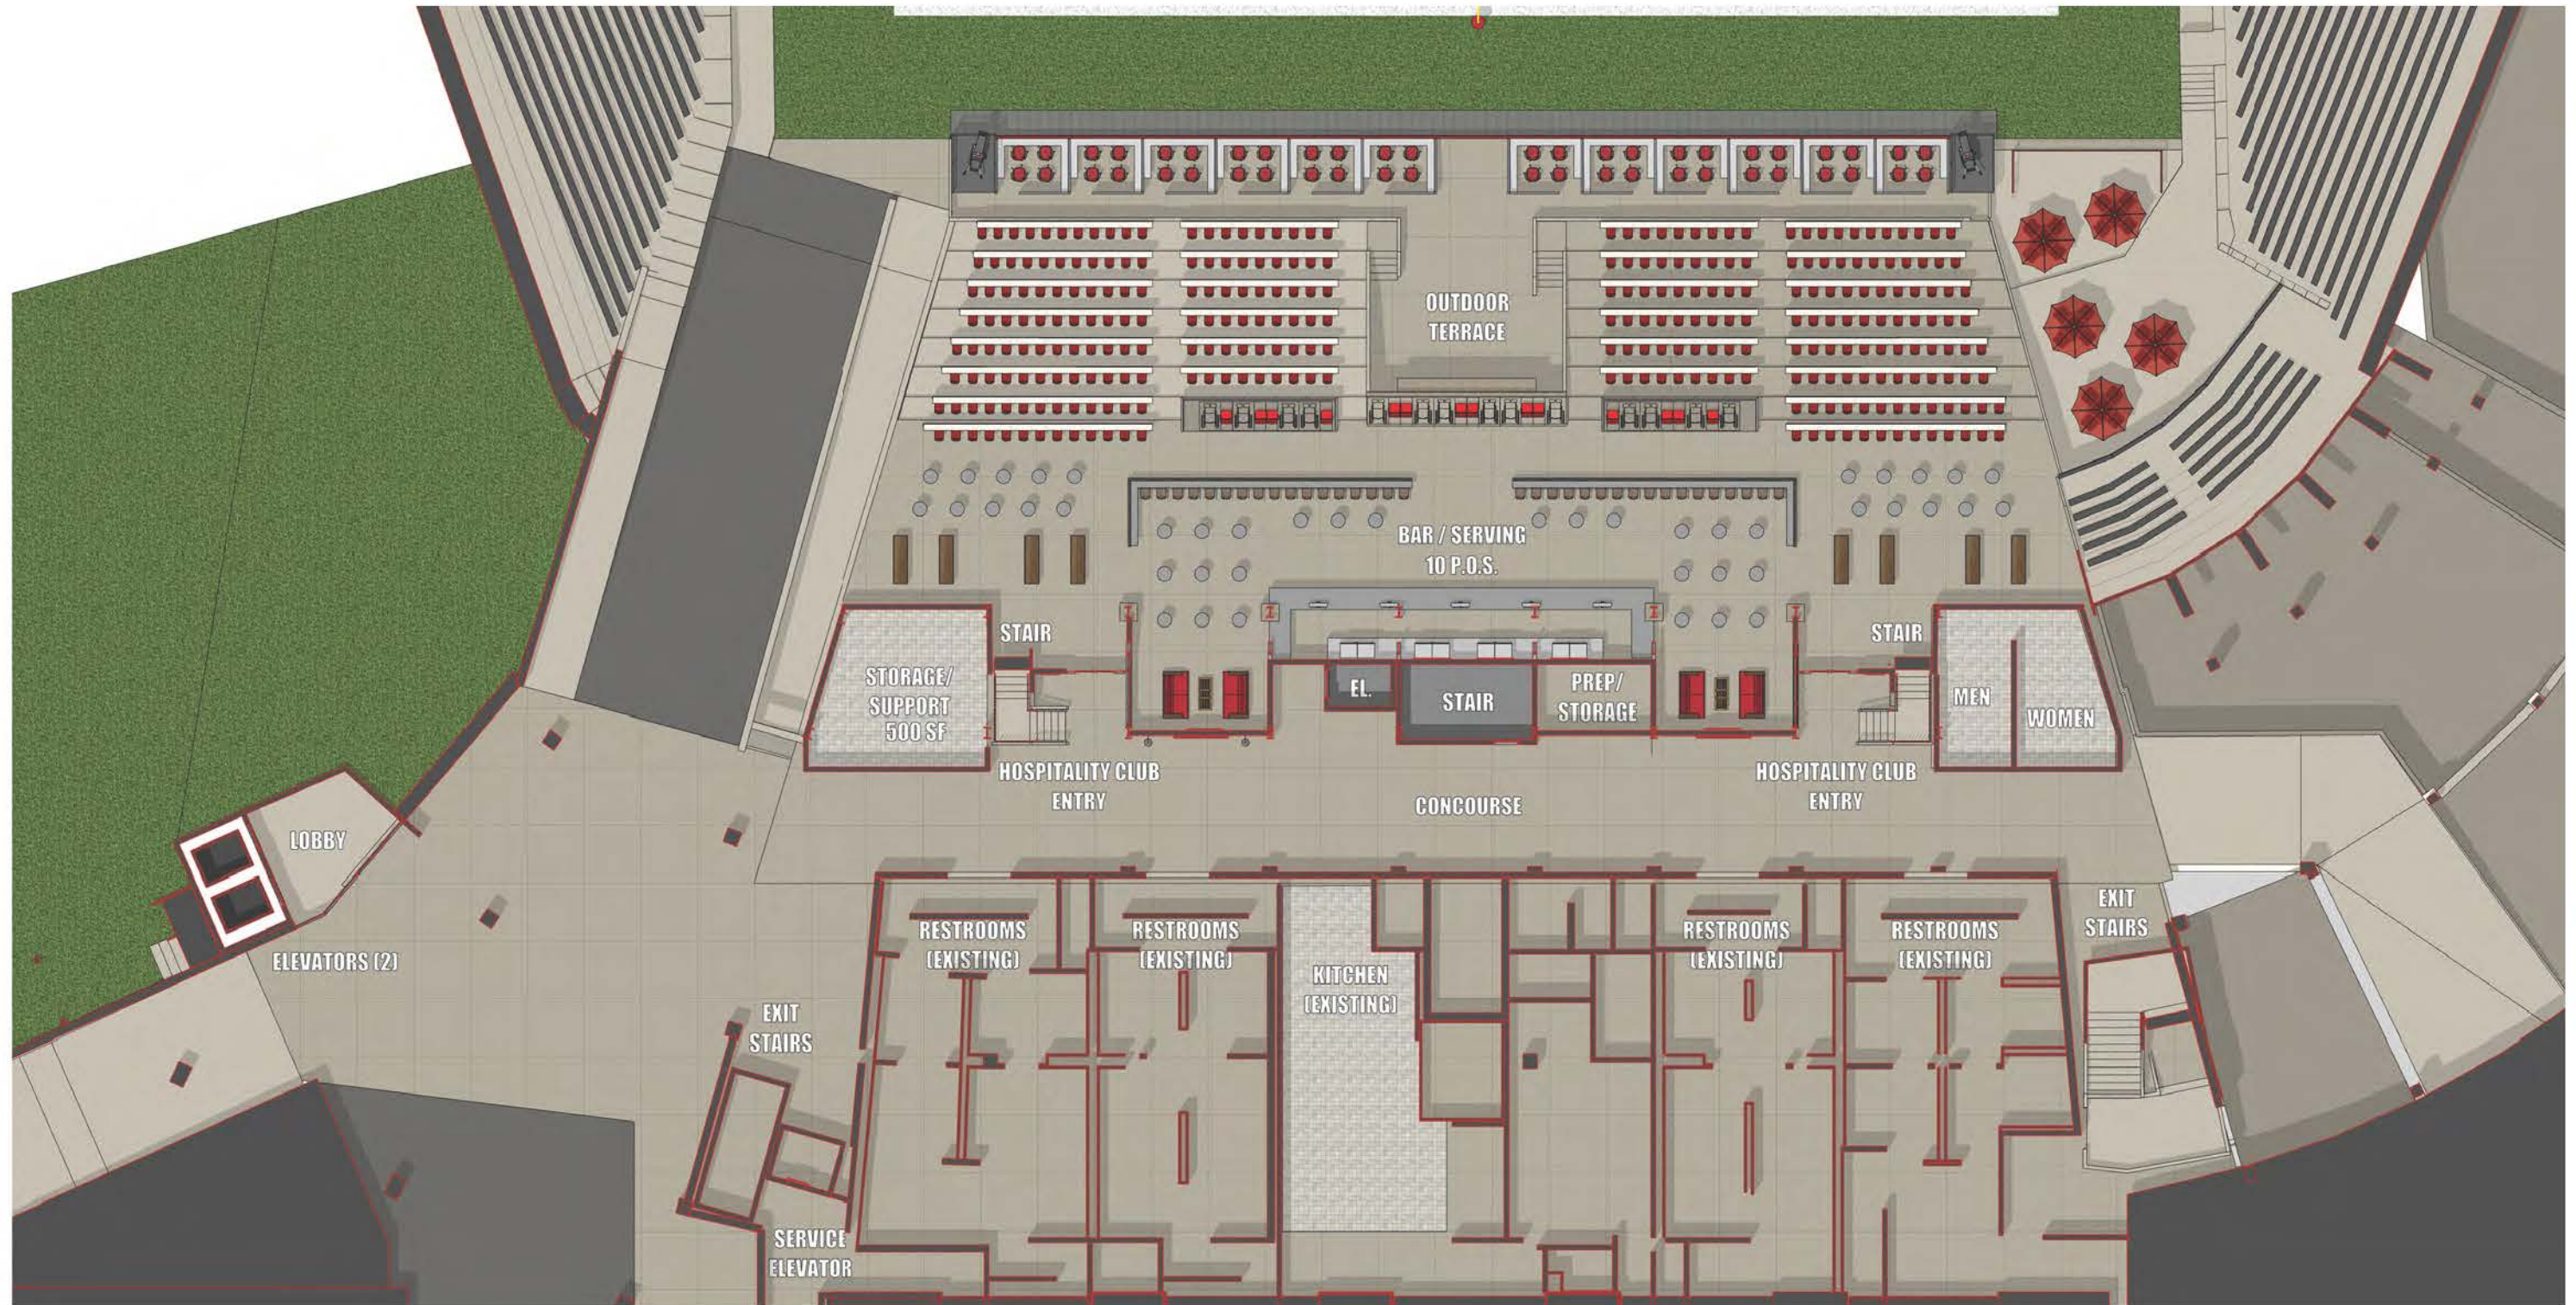

CONCOURSE LEVEL | FLOOR PLAN VIEW

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
 APRIL 29, 2020




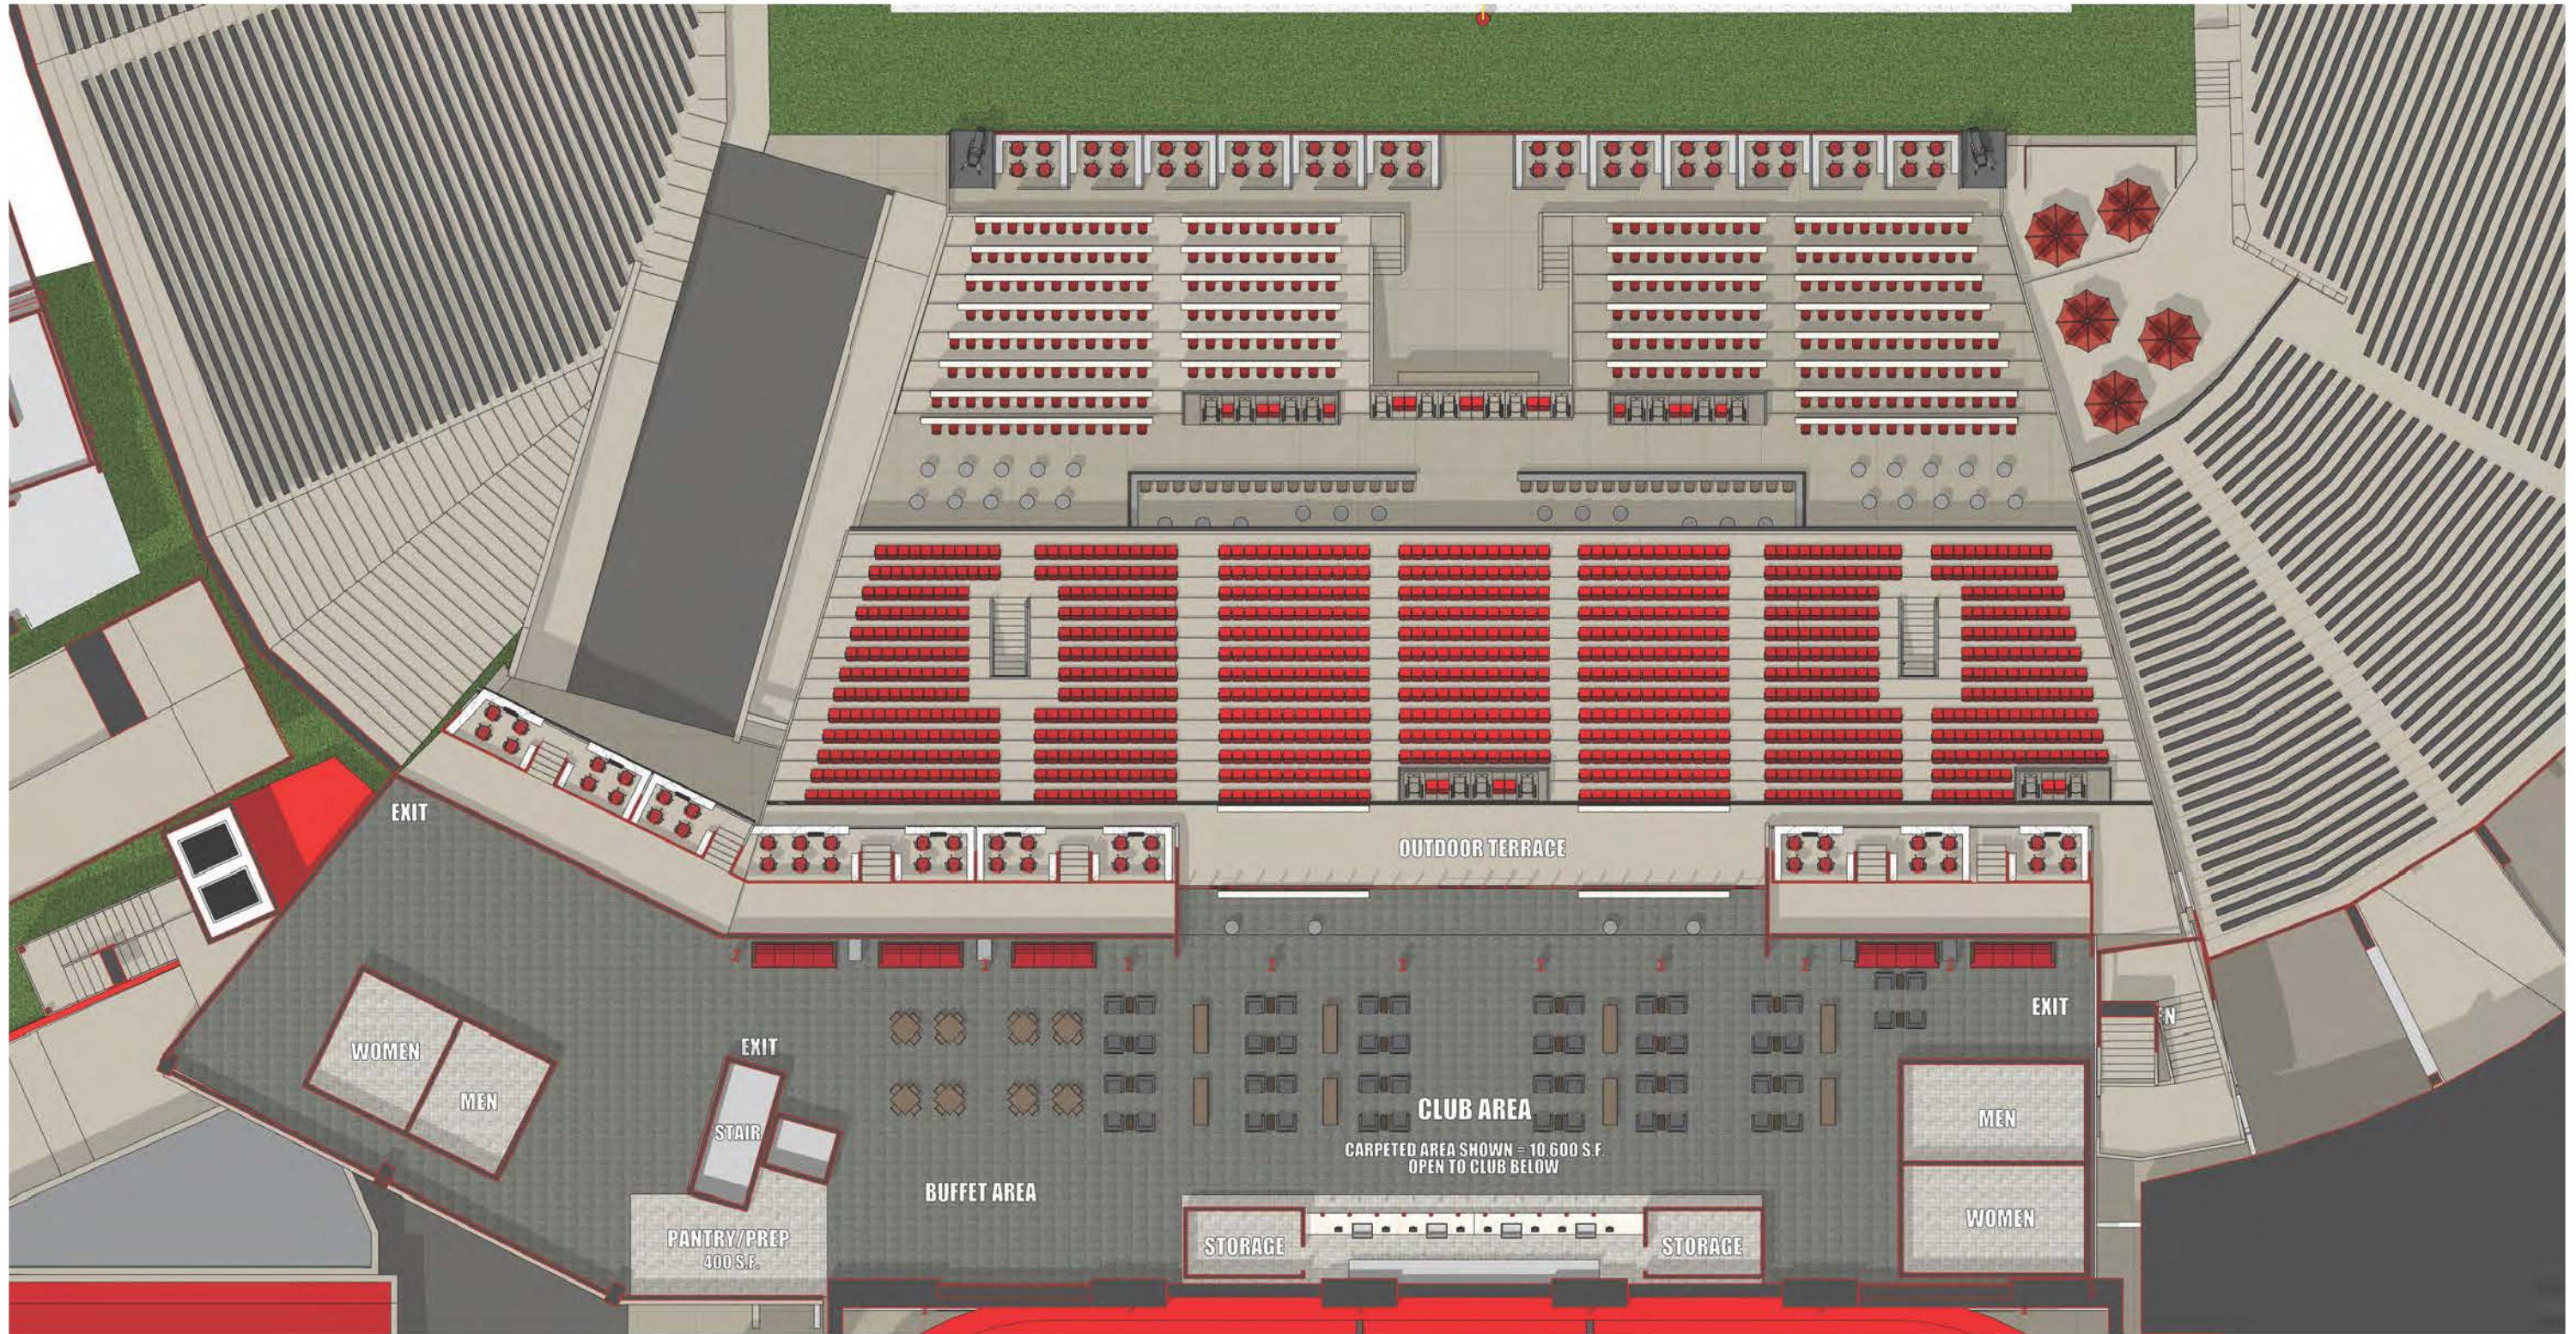

CLUB LEVEL | FLOOR PLAN VIEW

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020




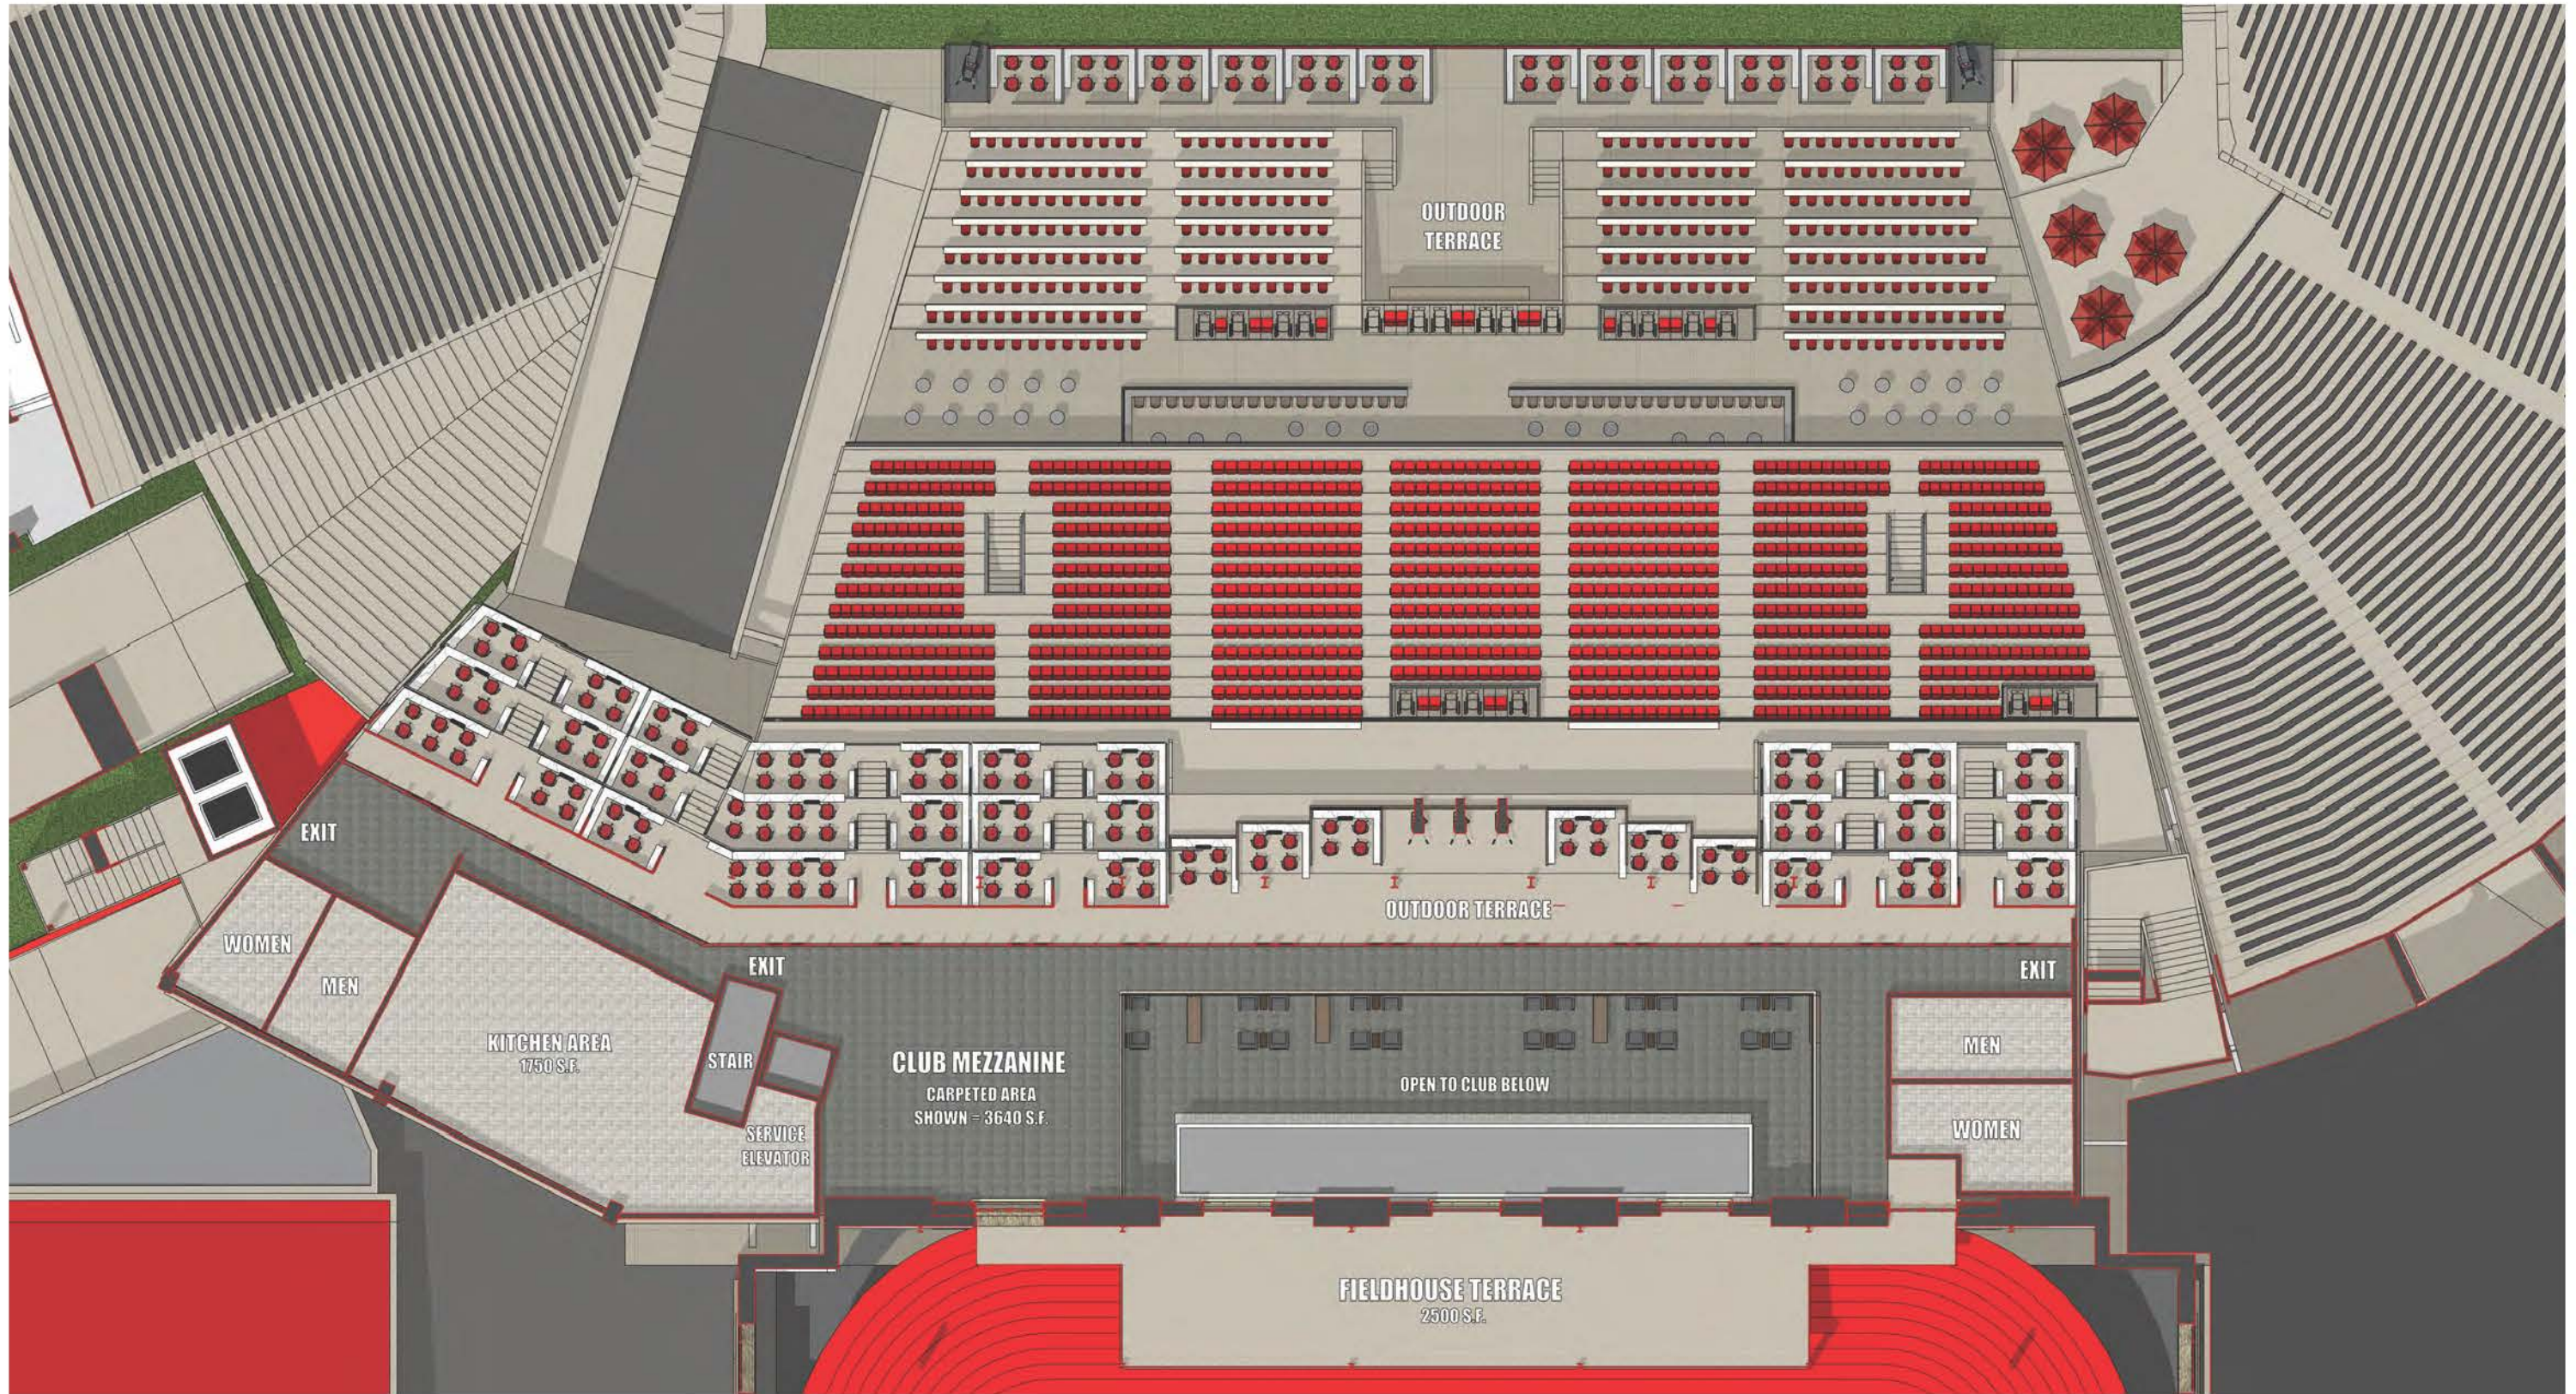

LOGE LEVEL | FLOOR PLAN VIEW

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
 APRIL 29, 2020



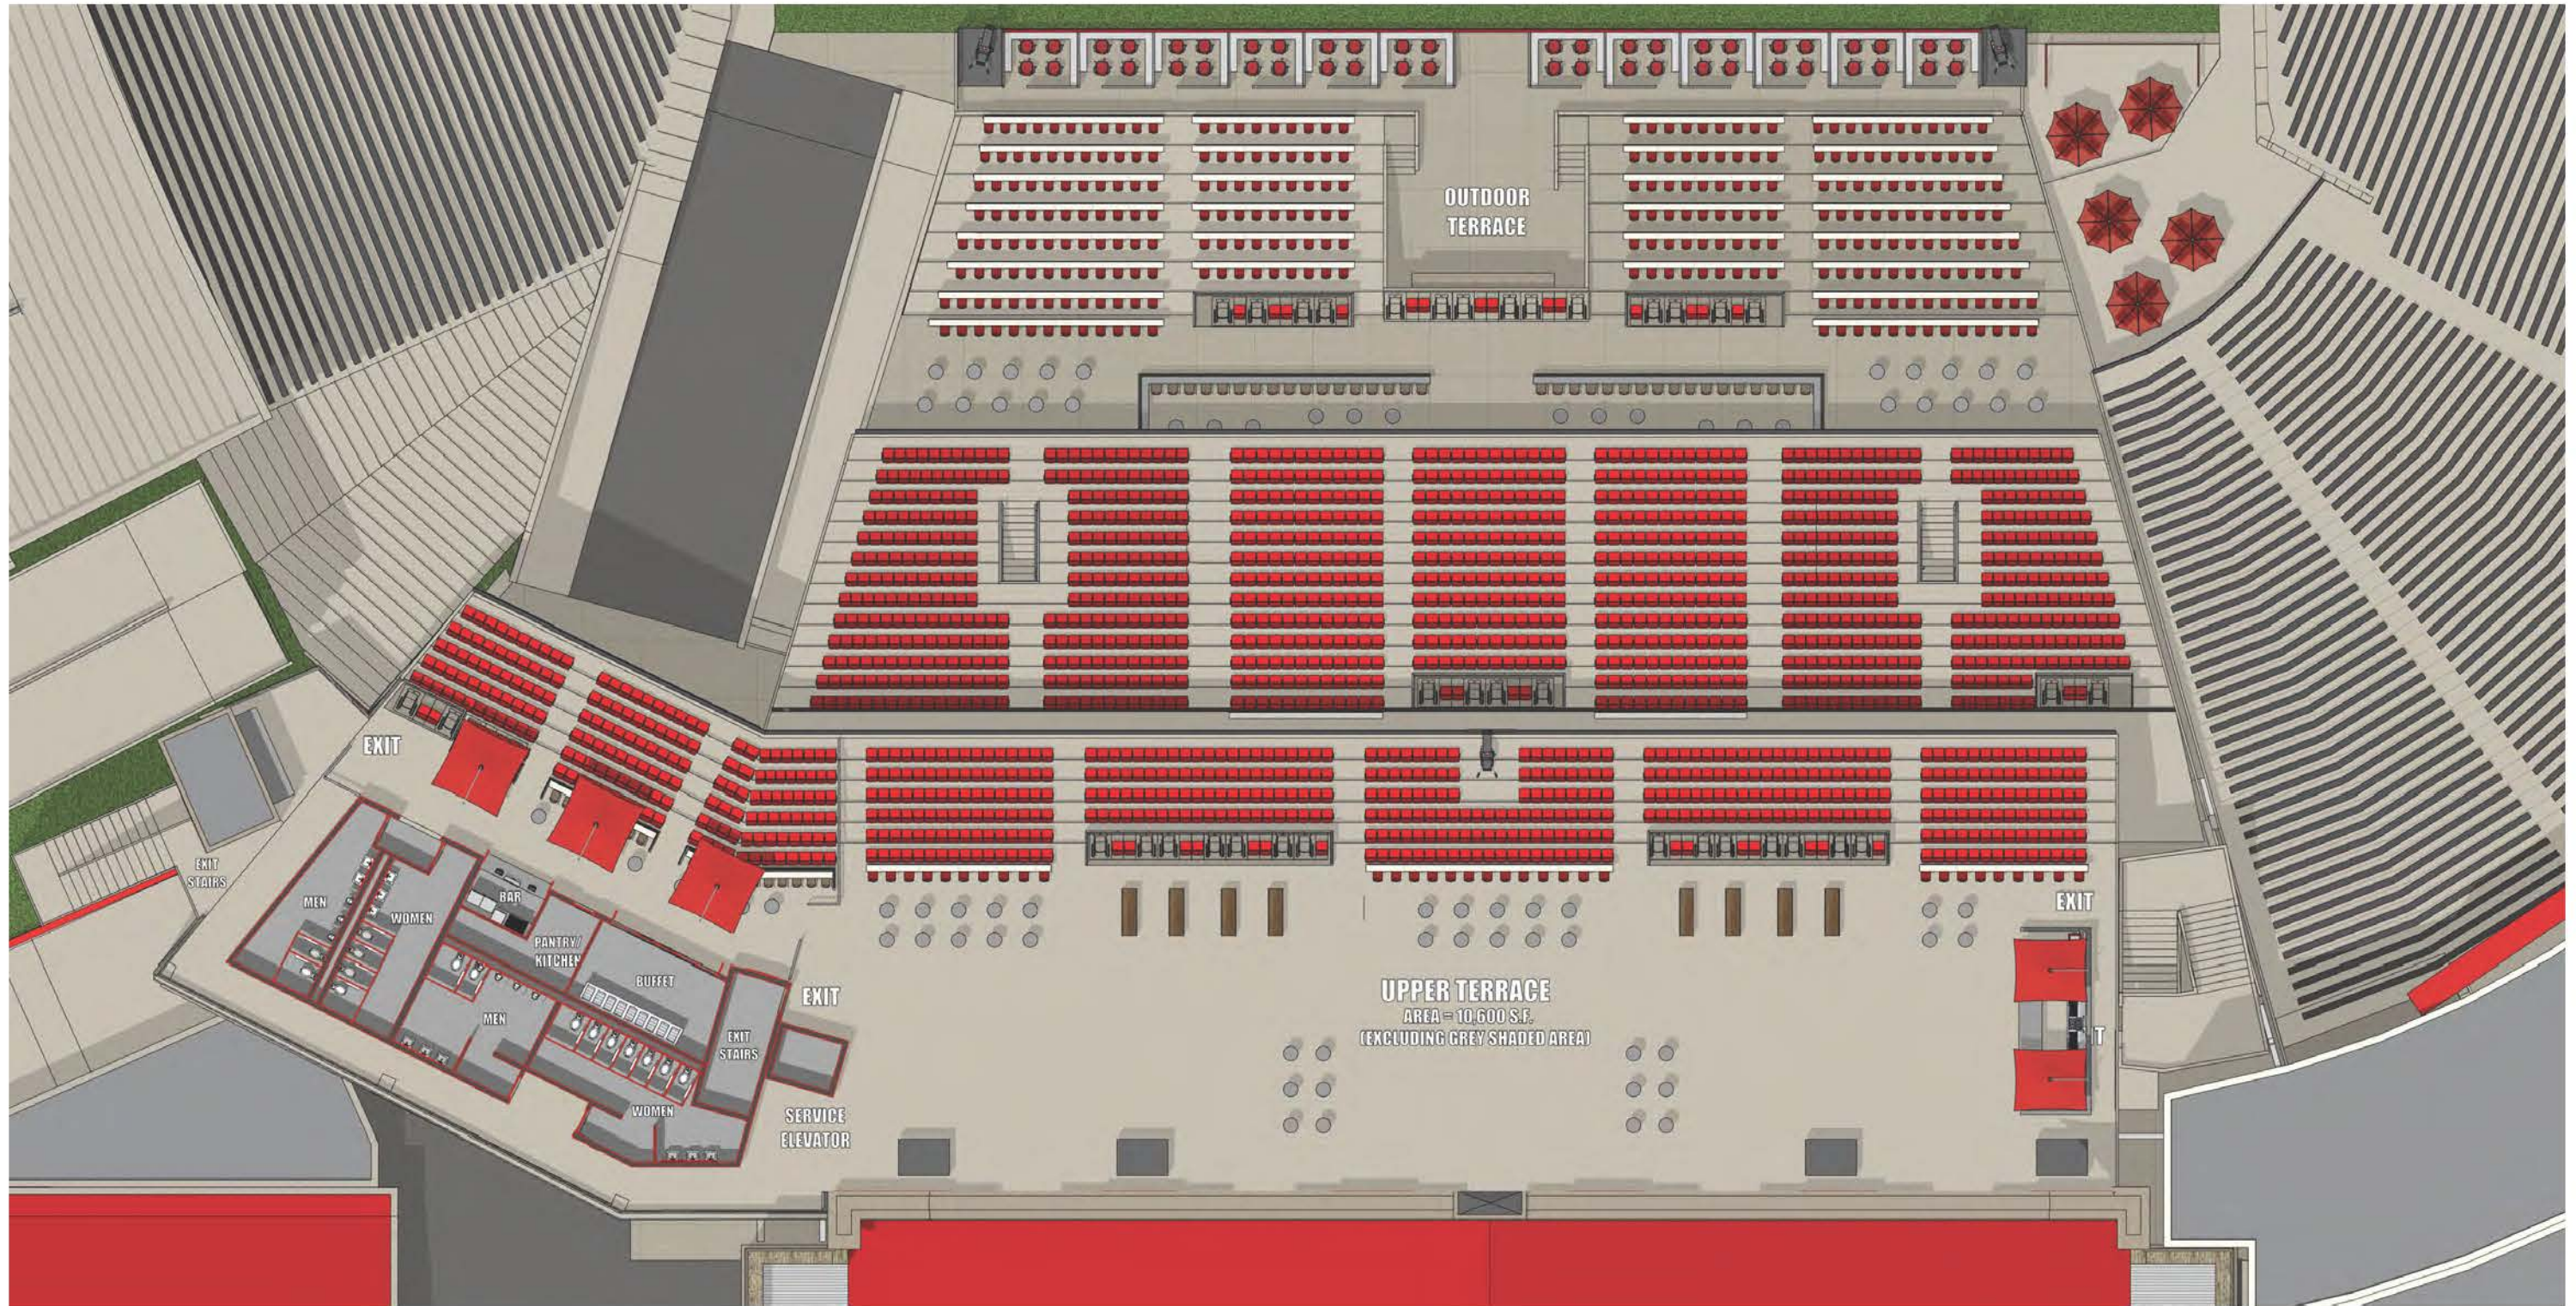

TERRACE LEVEL | FLOOR PLAN VIEW

19F2Y | CAMP RANDALL STADIUM RENOVATION PROJECT
APRIL 29, 2020



Page 1 of 3		Camp Randall South Endzone Renovation				Data Date 01-Jan-20	Run Date 27-Jan-20																									
Activity ID	Activity Name	Rem Dur	Start	Finish	2020												2021												2022			
					F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	
CAMP RANDALL S ENDZONE		0																														
Resources		135	29-Jan-20	06-Aug-20																												
A3910	In-Person Interviews	1	29-Jan-20*	29-Jan-20	In-Person Interviews																											
A3920	Letter of Intent Issued	1	12-Feb-20*	12-Feb-20	Letter of Intent Issued																											
A3940	Contract Negotiations	20	13-Feb-20	11-Mar-20	☐ Contract Negotiations																											
A4340	Design and Core Team Meetings	120	19-Feb-20*	06-Aug-20	█ Design and Core Team Meetings																											
A3720	Design-Build Award	1	25-Feb-20	25-Feb-20	Design-Build Award																											
A3930	Projed Kick Off Meeting	1	25-Feb-20*	25-Feb-20	Project Kick Off Meeting																											
Design & Pre-Construction		160	13-Feb-20	28-Sep-20																												
A3730	Design BP#1 Demo Foundations, Structure (Pull Ahead)	100	13-Feb-20	02-Jul-20	█ Design BP#1 Demo Foundations, Structure (Pull Ahead)																											
A3870	Program Verification	50	13-Feb-20	22-Apr-20	☐ Program Verification																											
A4080	Design BP#2 MEPF Trades	60	13-Feb-20	06-May-20	█ Design BP#2 MEPF Trades																											
A4110	Design BP#3 Artificial Turf	20	26-Feb-20	24-Mar-20	☐ Design BP#3 Artificial Turf																											
A4360	Design BP#3 Furniture	50	26-Feb-20	05-May-20	☐ Design BP#3 Furniture																											
A4230	Design BP#4 LED Boards	20	25-Mar-20	21-Apr-20	☐ Design BP#4 LED Boards																											
A4260	Design BP#5 Long Lead Items (Elev, Seats, Kitchen, Etc)	40	22-Apr-20	17-Jun-20	☐ Design BP#5 Long Lead Items (Elev, Seats, Kitchen, Etc)																											
A3790	Design BP#6 Finishes	60	06-Jul-20	28-Sep-20	☐ Design BP#6 Finishes																											
A3810	Design BP#7 Enclosure	50	06-Jul-20	14-Sep-20	☐ Design BP#7 Enclosure																											
Procurement		151	25-Mar-20	26-Oct-20																												
A4120	Bid BP#3 Artificial Turf	20	25-Mar-20	21-Apr-20	☐ Bid BP#3 Artificial Turf																											
A4240	Bid BP#4 LED Boards	20	22-Apr-20	19-May-20	☐ Bid BP#4 LED Boards																											
A4350	Bid BP#3 Furniture	20	06-May-20	03-Jun-20	☐ Bid BP#3 Furniture																											
A4100	Bid BP#2 MEPF Trades	20	07-May-20	04-Jun-20	█ Bid BP#2 MEPF Trades																											
A4090	Bid BP#1 Demo Foundations, Structure	20	06-Jul-20	31-Jul-20	☐ Bid BP#1 Demo Foundations, Structure																											
A4290	Bid BP#7 Enclosure	20	15-Sep-20	12-Oct-20	☐ Bid BP#7 Enclosure																											
A4270	Bid BP#5 Long Lead Items	20	29-Sep-20	26-Oct-20	☐ Bid BP#5 Long Lead Items																											
A4280	Bid BP#6 Finishes	20	29-Sep-20	26-Oct-20	☐ Bid BP#6 Finishes																											
Shop Drawings		0																														
Approval		156	06-Jan-20	12-Aug-20																												
A4040	WEPA-EIA Scoping Letter Sent	1	06-Jan-20*	06-Jan-20	WEPA-EIA Scoping Letter Sent																											
A4050	WEPA-EIA Draft released for Public Review	1	02-Mar-20*	02-Mar-20	} WEPA-EIA Draft released for Public Review																											

Actual Work
 Remaining Work
 Critical Remaining Work

JPC - BSA - HOK

JPC Progress Meetings
TASK filter: JPC Remaining Activities.



Camp Randall South Endzone Renovation

Data Date 01-Jan-20

Run Date 27-Jan-20

Activity ID	Activity Name	Rem Dur	Start	Finish	2020												2021												2022						
					F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A				
A3850	Stairs and SOG at Field Level	20	04-Feb-21	03-Mar-21													<input type="checkbox"/> Stairs and SOG at Field Level																		
A3680	Turf Camp Randall	45	17-May-21	20-Jul-21													<input type="checkbox"/> Turf Camp Randall																		
A3690	Turf McClain	42	03-Jan-22	01-Mar-22																									<input type="checkbox"/> Turf Mc						
Structure					226					13-Jul-20					28-May-21																				
A3540	MEPF Removals and Rerouting (Cable Tray)	60	13-Jul-20	05-Oct-20													<input checked="" type="checkbox"/> MEPF Removals and Rerouting (Cable Tray)																		
A4130	Site 8 Foundations (Accelerated)	15	03-Aug-20	21-Aug-20													<input type="checkbox"/> Site 8 Foundations (Accelerated)																		
A3530	Temp Enclosure of Mechanical Room	40	24-Aug-20	19-Oct-20													<input type="checkbox"/> Temp Enclosure of Mechanical Room																		
A4300	***Last Home Game 2020 - Nebraska***	0		21-Nov-20													<input checked="" type="checkbox"/> ***Last Home Game 2020 - Nebraska***																		
A3550	Remove Turf, Bleachers & Misc	10	23-Nov-20	07-Dec-20													<input type="checkbox"/> Remove Turf, Bleachers & Misc																		
A3630	Set Up Large Crane	5	23-Nov-20	30-Nov-20													<input type="checkbox"/> Set Up Large Crane																		
A3570	Site 7 Demo Structure at Grade	15	08-Dec-20	29-Dec-20													<input type="checkbox"/> Site 7 Demo Structure at Grade																		
A4140	Site 8 Demo Precast (SW Ramp)	5	15-Dec-20	21-Dec-20													<input type="checkbox"/> Site 8 Demo Precast (SW Ramp)																		
A3560	Site 7 Demo Precast Structure	25	30-Dec-20	03-Feb-21													<input type="checkbox"/> Site 7 Demo Precast Structure																		
A3610	Structure Prep - Columns/Dowels/Anchor Bolts	15	04-Feb-21	24-Feb-21													<input type="checkbox"/> Structure Prep - Columns/Dowels/Anchor Bolts																		
A3620	Site 7 Set New Structure (Upper)	35	25-Feb-21	14-Apr-21													<input type="checkbox"/> Site 7 Set New Structure (Upper)																		
A4150	Move Large Crane	2	15-Apr-21	16-Apr-21													<input type="checkbox"/> Move Large Crane																		
A4310	Set Up RT Crane	2	15-Apr-21	16-Apr-21													<input type="checkbox"/> Set Up RT Crane																		
A3590	Site 7 Field Club Foundations	20	19-Apr-21	14-May-21													<input type="checkbox"/> Site 7 Field Club Foundations																		
A4160	Site 8 Set New Structure	10	19-Apr-21	30-Apr-21													<input type="checkbox"/> Site 8 Set New Structure																		
A3670	Remove Large Crane	5	03-May-21	07-May-21													<input type="checkbox"/> Remove Large Crane																		
A3600	Site 7 Structure of Field Club (Lower)	10	17-May-21	28-May-21													<input type="checkbox"/> Site 7 Structure of Field Club (Lower)																		
Skin					275					14-May-20					14-Jun-21																				
A3650	Field House North Facade Work	60	14-May-20	10-Aug-20													<input type="checkbox"/> Field House North Facade Work																		
A3640	Site 7 Traffic Coating & Building Enclosure (Upper)	25	15-Apr-21	19-May-21													<input type="checkbox"/> Site 7 Traffic Coating & Building Enclosure (Upper)																		
A4210	Site 8 Enclosure	20	10-May-21	07-Jun-21													<input type="checkbox"/> Site 8 Enclosure																		
A3700	Site 7 Traffic Coating & Building Enclosure (Lower)	10	01-Jun-21	14-Jun-21													<input type="checkbox"/> Site 7 Traffic Coating & Building Enclosure (Lower)																		
Finishes					75					20-May-21					04-Sep-21																				
A3660	Site 7 Interior Finishes (Upper)	35	20-May-21	09-Jul-21													<input type="checkbox"/> Site 7 Interior Finishes (Upper)																		
A4190	Site 7 Exterior Finishes & Seating (Upper)	30	20-May-21	01-Jul-21													<input type="checkbox"/> Site 7 Exterior Finishes & Seating (Upper)																		
A4220	Site 8 Finishes	25	08-Jun-21	13-Jul-21													<input type="checkbox"/> Site 8 Finishes																		
A4330	Install Elevators	45	08-Jun-21	10-Aug-21													<input type="checkbox"/> Install Elevators																		
A4200	Site 7 Exterior Finishes & Seating (Lower)	20	15-Jun-21	13-Jul-21													<input type="checkbox"/> Site 7 Exterior Finishes & Seating (Lower)																		
A4170	Site 7 Interior Finishes (Beer Garden)	20	02-Jul-21	30-Jul-21													<input type="checkbox"/> Site 7 Interior Finishes (Beer Garden)																		
A4180	Site 7 Interior Finishes (Lower)	25	02-Jul-21	06-Aug-21													<input type="checkbox"/> Site 7 Interior Finishes (Lower)																		
A4320	***First Home Game 2021 - Penn State***	0	04-Sep-21														<input checked="" type="checkbox"/> ***First Home Game 2021 - Penn St																		

